

APPLICATION FOR U.S. PATENT
TRANSMITTAL FORM

Box Patent Application
ASSISTANT COMMISSIONER
OF PATENTS
Washington, D.C. 20231

Sir:

Transmitted herewith for filing is the original patent application of:

Inventors: Harriet E. Brichta
Floyd Phillip Littlefield, Jr.
Bruce W. Bradbury
Iveoma C. Eriken
Julio A. Rodriguez

For: SYSTEM AND METHOD OF MANAGING A PROGRAM OFFICE


Enclosed are: Specification, Claims and Abstract (55 pages)
35 Sheets of Formal Drawings
Declaration of Inventorship
Assignment, and Transmittal Therefor

FEE CALCULATION					FEE
	Number		Number Extra	Rate	Basic Fee
					\$760.00
Total Claims:	62	- 20 =	42	X \$18 =	\$756.00
Independent Claims	3	- 3 =	0	X \$78 =	\$0.00
TOTAL FILING FEE =					\$1,516.00

Please charge the filing fee of \$1,516.00, and any other fee required by this paper, or credit any overpayment, to Deposit Account No. 05-0765 of Electronic Data Systems Corporation.
A duplicate copy of this sheet is enclosed.

BAKER & BOTTS, L.L.P.
Attorneys for Applicants

February 3, 1999
Date


Wei Wei Jeang
Registration No. 33,305

SYSTEM AND METHOD OF
MANAGING AN OFFICE OF PROGRAMS

TECHNICAL FIELD OF THE INVENTION

This invention is related in general to the field of computer software systems, and more particularly, to a system and method of managing an office of programs.

BACKGROUND OF THE INVENTION

Large broad-scale programs that change particular aspects of the operation of a corporation pose significant challenges especially for those corporations that are geographically dispersed and functionally heterogenous. Change is an inevitable aspect of growth, but change must be implemented in a controlled fashion with minimal impact to production and throughput.

In many organizations, rather than micro-managing the change programs high in the organizational hierarchy, the responsibility is delegated down the chain of command. Downward delegation of the change oversight responsibility has many negative side-effects. First, major differences in regional policies may emerge. Second, decentralized change oversight can result in redundancies and inefficiencies. Even more importantly, decentralized change oversight may disadvantageously remove the organization's capability to manage costs, schedules, and resources globally across the entire organization.

Known project management methodologies provide substantial value in managing change at a micro-level. Some project management programs such as Microsoft

Project™, Computer Associate's Super Project™, and SAP™, attempt to integrate projects to produce a consolidated view. However, these programs are very limited. By far, the most restrictive feature of conventional project management programs requires all participating business units to use identical project management methodology, often with identically defined parameters. In the real world, such limitations are impractical and difficult to implement for an international organization of any meaningful size. Furthermore, such restrictions would be useless for consolidating the management of programs of existing projects.

SUMMARY OF THE INVENTION

It has been recognized that it is desirable to provide a program office management system and method that provide a corporation the capability to manage costs, schedules and resources from a micro- to a macro-level globally across the entire organization. The term "program office" or an office of programs is defined as an office or corporate entity that is responsible for managing, coordinating and delivering one or more mission critical functionalities or programs. A "program" is a collection of related projects. An example of a program is one that identifies and remediates systems that process century-date data incorrectly in the organization. The program office management system and method of the present invention function independently of project management methodology and data source which enable the incorporation and integration of pre-existing data and data sources in different formats.

In one aspect of the invention, a program office management system includes a program office database which stores:

informational data associated with accounts, projects, and programs;

financial data associated with the accounts, projects, and programs;

5 schedule and progress data associated with the accounts, projects, and programs;

data associated with personnel, roles, and security access information thereof;

10 data associated with translating progress milestones and tactics to reporting categories; and

update data associated with the progress, actual expenditures, and labor resources of the accounts, projects, and programs;

15 The system further includes a user interface operable to display data stored in the program office according to a predetermined security scheme based on the security access information stored in the program office database, and further operable to receive the update data on a periodic basis.

20 In another aspect of the invention, a method of managing a program office includes the steps of storing and accessing data associated with at least one project in a program office database, including informational data, financial data, schedule and progress data associated with
25 the at least one project; storing update data associated with the at least one project; identifying persons associated with the at least one project, assigning at least one role relevant to the at least one project to each person, and storing data associated with the persons and
30 their assigned roles in the program office database; and mapping tactic and milestones defined in the at least one project to tactic types and milestone categories defined in the program office database for reporting purposes.

35 In yet another aspect of the invention, a system for managing at least one program including a plurality of

projects for at least one account are provided. The system includes at least one program office database which stores:

informational data associated with the accounts, projects, and programs;

5 financial data associated with the accounts, projects, and programs;

schedule and progress data associated with the accounts, projects, and programs;

10 personnel data associated with persons having responsibility associated with the accounts, projects, and programs, the personnel data including a unique person identifier for each person;

15 security data having an assignment of at least one role to each person and an assignment of at least one update authorization to certain persons having oversight responsibility;

data associated with translating progress milestones defined in the projects to tactics defined in the system; and

20 update data associated with the progress, actual expenditures, and labor resources of the accounts, projects, and programs;

25 The system further includes at least one user interface operable to display and allow access to the data stored in the program office according to a predetermined security scheme based on the person identifier, role and update authorization assignment stored in the at least one program office database, and further operable to receive the update data on a periodic basis.

30 One technical advantage of the invention is that there is no requirement of using identical project management methodology or data sources. Milestones unique to particular projects may be translated to industry standard milestones appropriate for the program(s). Organizational
35 costs, schedules and resources can be managed and

controlled across the organization on many levels. Further, access to system data is securely and strictly controlled based on a user's identifier, the user's role(s), and authorization levels. Another technical
5 advantage of the present invention is the ability to archive seemingly limitless project history with minimal data storage. Priority can be assigned to projects in the entire organization to allocate resources.

For a better understanding of the present invention, reference may be made to the accompanying drawings, in which:

FIGURE 1 is a top level block diagram of an embodiment of the present invention;

FIGURE 2 is a more detailed block diagram of an embodiment of the present invention showing certain data update processes;

FIGURE 3 is a block diagram showing the exemplary files and folders used and manipulated during an embodiment of the self-extracting data update processes;

FIGURE 4 is a schematic block diagram of a representation of components in a program office;

15 FIGURE 5 is an exemplary view of a log in screen of
the web user interface;

FIGURE 6 is an exemplary view of a home page screen of the web user interface;

FIGURE 7 is an exemplary view of an add person and
20 assign roles screen of the web user interface;

FIGURE 8 is an exemplary view of an add person screen of the web user interface;

FIGURE 9 is an exemplary view of an assign role screen of the web user interface;

25 FIGURE 10 is an exemplary view of an update
authorizations screen of the web user interface;

FIGURE 11 is an exemplary view of an add account screen of the web user interface;

FIGURE 12 is an exemplary view of an account forecast
30 screen of the web user interface;

FIGURE 13 is an exemplary view of an account actuals screen of the web user interface;

FIGURE 14 is an exemplary view of an update account actuals screen of the web user interface;

FIGURES 15A-15F are an exemplary views of add project screens of the web user interface;

FIGURE 16 is an exemplary view of an update budget and labor actuals screen of the web user interface;

5 FIGURE 17 is an exemplary view of an update schedules and progress actuals screen of the web user interface;

FIGURE 18 is an exemplary view of a home screen of the self-extracting user interface;

10 FIGURE 19 is an exemplary view of a view or revise account forecasts screen of the self-extracting user interface;

FIGURE 20 is an exemplary view of an update account actuals screen of the self-extracting user interface;

15 FIGURE 21 is a data model of an embodiment of the program office database;

FIGURE 22 is a relational data model of an embodiment of the program office database;

FIGURE 23 is an exemplary view of a home screen of the program office interface;

20 FIGURE 24 is an exemplary view of a form screen for project selection criteria via the program office interface;

FIGURE 25 is an exemplary view of a form screen for entering project data via the program office interface;

25 FIGURE 26 is an exemplary view of a screen for viewing project forecasts via the program office interface;

FIGURE 27 is an exemplary view of a screen for viewing project milestone dates via the program office interface;

30 FIGURE 28 is an exemplary view of a screen for viewing project milestone actuals via the program office interface;

FIGURE 29 is an exemplary view of a screen for entering project and program cross-reference data via the program office interface; and

64-99-001-0344

FIGURE 30 is an exemplary view of a screen for creating a project detail report via the program office interface.

5 DETAILED DESCRIPTION OF THE INVENTION

Referring to FIGURE 1, a block diagram of an embodiment of the system and method of managing a program office 10 of the present invention is shown. System 10 includes a program office database 12, which includes a data structure having tables and data fields storing data used in the present invention. Relational database, or object-oriented database, object-relational database or any other suitable database scheme may be used. The data structure and the data are described in more detail below. One or more program office interfaces 13 may be used to access, update, view, and retrieve data residing in program office database 12. Program office interface 13 is primarily used by upper level management, internal auditors, and external auditors. A front-end 14 including user interfaces 15 and 16 are provided to users to primarily submit update data to program office database 12. In an exemplary embodiment, front-end 14 may be web-based as well as user interface 15. At least one web user interface 15 allows users to primarily add, change or update people information, account information, and project information. Web user interface 15 runs on a web server as a web browser-based system. User interface 16 is a self-extracting user interface that may be a spread sheet-based interface that is capable of running on a computer system with minimal system requirements. One or more sub-databases 17 may be substantial duplicate copies or a subset of program office database 12. Sub-databases 17 may be accessible by one or more web front-ends 14 and their respective web user interfaces and self-extracting user

interfaces, which may be located geographically remote from program office database 12.

Program office database 12 may be electronically linked to other project management tools 19 or other data sources 29 to extract or import data. This database access may be achieved by open database connectivity (ODBC) using structured query language (SQL) or another suitable query language. Program office database 12 may include logic tables or logical views of certain data fields in program office database 12 and data tables encompassed in project management tools 19 and/or other data sources 29. These views, when executed, retrieve the data from these data fields and data tables from project management tools 19 and/or other data sources to program office database 12. Alternatively, application program interfaces (API) 27 tailored to the specific project management tools 19 may be provided for accessing data stored therein. In this manner, it is not necessary to duplicate data already stored and maintained in project management tools 19 and other data sources 29 in program office database 12. The data may be imported into program office database 12 only when needed for viewing or reporting purposes.

The system of the present invention may also import data from other data sources 29 stored and maintained by other departments within the organization, such as human resources and cost accounting databases, to obtain data needed for reporting and auditing purposes. Program office interface 13 can therefore access the necessary data to independently verify and audit the actual and budget data from program office database 12.

Referring to FIGURE 2, a block diagram providing a more detailed description of some of the exemplary processes involved to update program office database 12 is shown. Using web user interface 15 through web front-end 14, a browser-based tool may be used to perform the

functions shown: add people and assign roles, add accounts, add projects, provide periodic updates, revise basic information, and revise forecasts. Through web front-end 14, self-extracting user interface 16 may be obtained or extracted.

Referring to both FIGURES 2 and 3, a person having a sufficiently senior role in a role hierarchy such as a coordinator 18 may select an extract function of web front-end 14 and extracts an executable of user interface 16. It is important to note that the roles described herein are merely examples, such as program manager, coordinator, project manager, and account manager, and these roles are representative of levels in a role hierarchy. In the role hierarchy, the roles are capable of performing increasing scope of functionality. For example, a coordinator is a project-level manager that may be assigned the authority to add people to program office database 12, assign roles for a business unit, and add projects and accounts for business units, but an account manager may not perform these same functions. User interface 16 may be a self-extracting executable file which may be based on a spread sheet application such as Microsoft Excel™.

The extracted user interface 16 may include two spread sheet files, a spread sheet file 20 with the coordinator's user identifier and a consolidated data file 21. The extracted user interface 16 may also include four folders: input folder 22, backup folder 23, output folder 24, and split folder 25. Split folder 25 holds individual account files extracted from web front-end 14. Split folder 25 is used to split into one or more account files 26, which are distributed to account managers who have oversight responsibilities of the accounts. Because some managers may have oversight responsibility of more than one account, the split account files for those managers will include one file for each account identified with the account manager's

user identifier and a serial number to identify the account. The manner split account files 26 are distributed may be electronically via file transfer protocol, as an E-mail attachment, over a network, on a diskette, or any other means convenient to the responsible recipient and agreed upon between the requestor and the responsible recipient. The account managers may then view and modify data according to the assigned security authorization. Typically, a periodic update is requested from the account managers, such as a monthly report of milestones reached, revise project forecasts, update budget and labor actual expenditures, and update schedule and progress.

After all the new and changed data are entered and modified, the account managers submit the update data. The result may be one or more text files that contains all the update data. These text files are put into input folder 22 by coordinator 18. Using web user interface 15, coordinator 18 also verifies that all account files 26 have been returned each time period by the subordinate managers. The returned account files in input folders 22 are automatically consolidated by activating the consolidate function in web user interface 15 and into a single file, which is then automatically transferred to output folder 24, and a copy of which is automatically stored in backup folder 23. After the consolidate process, coordinator 18 then uses web front-end 14 to import or upload the consolidated data files from output folder 24 to program office database 12. As shown in FIGURE 2, reports 11 containing data from program office database 12 may be viewed, printed or displayed. Program office database 12 may also be linked to project management tools 19 to obtain or provide data.

Referring to FIGURE 4, a block diagram of an exemplary program office 40 under the management and control of the system and method of the present invention is shown. A

corporation is made up of one or more business units 42. Each business unit 42 may have zero or more accounts 44 that contribute to the program cost recovery through the revenues 46 they generate on behalf of the program. These revenues 46 may be clearly distinguishable from revenues derived from other sources. The difference between the program revenues and expenses is hereinafter referred to as the program contribution for business unit 42. All business units 42 have a value 48 they contribute to the corporation that may be measured empirically through current revenues, earnings and profits, indirectly through forecasts of expected future revenues, earnings and profits, indirectly through delivery of support services utilized by the corporation, or by any other means deemed appropriate by the senior leadership of the corporation.

All business units 42 utilize one or more systems 50 to deliver value 48 to the corporation. Systems 50 may be evaluated and weighted in terms of how important they are in delivering value to the corporation. All systems 50 may include one or more identifiable components 52 of component types 54 which are remediated or changed by projects 56. A system 50 may be remediated or changed by one or more projects 56, and a project 56 may remediate or change one or more systems 50.

One or more business units 42 may be responsible for the cost of remediating or changing systems 50 through projects 56. These business units 42 are referred to as the business owners of projects 56. Business units 42 have people 58 that form project teams 62. Each person may be assigned one or more roles. The roles define the functionality that the role-holders may perform. However, the role-holders may perform these functionality only with the setting of an authority flag, or the update authority. The setting of the update authority flag or the granting of the update authority is the responsibility of senior level

management personnel. Project teams 62 may utilize project management tools 64 to manage and complete projects 56 that remediate or change systems 50. In the present invention, project management tools 64 may be any tool using any project management methodology. In other words, all projects 56 may be managed by the present system and method regardless of the project management methodology.

Costs are aggregated across business units 42 by program 64 for financial accounting, fiscal audits, management oversight, and reporting. Projects 56 may belong to one or more programs 64. Projects 56 that are financially aggregated under one or more program 64 may have an impact on another program 64. If the financially liable programs are outside the scope of the program office, budgets, expenditures, and staffing need not be collected, although collection of such data may still be performed. However, all projects 56 impacting a program 64 may report project schedules and milestone progress, since they impact the overall success or failure of program 64.

Using the present invention, projects 56 may be prioritized in terms of the value they contribute to the corporation based on systems 50 changed by projects 56 as evaluated by business units 42 utilizing system 50 to deliver value 58. Projects 56 may also be prioritized in terms of the contingency costs associated with failure to deliver the project. Projects 56 may be aggregated in terms of the quantity and type of work components 52 required to deliver program 64. Shortages by component type can be predicted based on need and burn rate. Burn rate is a value that provides information on whether resources are expended efficiently in terms of the progress made so far and what remains to complete the project. Using the system and method of the present invention, it is possible to more easily recognize projects of similar functions undertaken by the organization that may be

redundant or duplicative. Geographic areas may be examined to ensure they have adequate coverage of the critical functional areas required to conduct business and deliver program 64. Unknowns related to projects 56 may be readily detected and thus eliciting a call to action. Projects 56 that are lagging in schedule progress are readily identifiable and may be merged intelligently by function and/or geography as appropriate to deliver successful completion of program 64. Resources, including people 58, may be aligned to ensure completion of projects 56 with the highest priority.

Projects 56 may be remediated or changed using a variety of tactics. A tactic is a strategy or approach taken in the project to affect change. Tactics may be grouped into types. Examples of tactic types include repair, replace, outsource, retire, upgrade, and assess. Project management tools using different methodologies may define different tactics.

Milestones is a term that is used to measure progress and is evidenced by quantifiable and verifiable deliverables. A tactic therefore can be defined to have one or more milestones. Project management implementations using different methodologies may define different sets of milestones for their tactics.

In order to operate independently of different project management tools and methodologies and still be able to encompass the projects under the umbrella of the present system, the system and method of the present invention define milestone categories into which milestones defined in the project management tools may be mapped into. Examples of milestone categories may be assess, renovate, test, and implement. Corresponding to the milestone categories are tactic types defined in the present system and method. Tactic types can be defined in terms of the milestone categories required to complete a project of that

tactic type. Therefore, a tactic defined in any project management tool can be categorized as a tactic type defined in the present system, and then mapped into milestone categories defined in the present system. This mapping provides a translation across terminology boundaries as well as language boundaries. Therefore, a project may continue to be managed under a project management tool using different methodologies, terminologies, as well as using the native language of the project management team. Furthermore, account managers and project managers may continue to use the same terminology and provide update data to the present system using the same terminology. The mechanism for implementing this mapping or translation process is described in more detail below.

People fill one or more roles. Senior leadership such as a program manager may grant specific access and update authority to persons having specific roles with regard to specific projects in their business unit. Therefore, the granting of update authority is strictly controlled and can be performed only by senior management. One of the authorization levels granted is surrogate, which grants the grantee the same authorization as the grantor. Another authorization level is update authority, which gives the grantee the clearance to make changes or updates to certain data determined by the roles performed by the person. Using user identifiers, roles, and authorization levels, every step in every process is controlled based on rule, role and function. The rules of access are formulated based on roles of the user and the authorization level as well as the data manipulating function to be performed. Therefore, the data that people can view and modify is strictly defined and enforced. The rules used to enforce data integrity may be achieved with referential integrity tables, code implemented in a programming language, such as C++ or Visual Basic, or any

other suitable mechanism. Client side validation is utilized in web user interface on data to be submitted to program office database 12 to improve performance while ensuring data validity. The mechanism to implement the rule, role and function-based security is described in more detail below.

FIGURES 5-17 are sample screens of web user interface 15 which provide further insight on the construction and operation of the present invention. FIGURE 5 is an exemplary screen of the login screen, which requests the user to enter the user identifier (ID) and a password. From the user identifier, the user's role in one or more accounts or projects may be determined, and further the authorization level assigned to the user in each account is determined.

Hereinafter the description is directed to several exemplary screens that may be seen by users via the end user interfaces 15 and 16 and via program office interface 13. In general, the accessibility of data within program office database 12 is dependent on the assigned role of the user, whether the user has update authority, and the function the user desires to perform. For example, no one except for persons having a role at the top of the role hierarchy may assign or change roles to people. A person having a particular role typically may only view or change data at or below him or her in the hierarchy, if so authorized by the update authorization flag. An example is that a project manager may be authorized to change data associated with accounts, but an account manager may not be authorized to change data associated with projects. On the other hand, a person can typically change data related to him or herself. Some data are viewable by persons of certain roles but other data are inaccessible to them. For example, a business owner may see progress data associated with a business unit under the oversight responsibility of

another business owner, but the financial data are not available for view.

FIGURE 6 is an exemplary screen of the home page of web user interface 15. Four primary functions are listed: people, account, project, and reporting. The people function is further broken down into the functions of adding persons and assign roles, update authorizations, update personal data, and change password. The account function is further broken down into the functions of add accounts, revise account data, revise account forecasts, and update account actuals (what changes to account data actually took place). The project function is further broken down into the functions of add projects, revise basic data and forecasts, update budget and labor actuals, and update schedules and progress actuals (what progress actually was achieved). The reporting function provides the function of extracting information from the database to put together reports or logical views of the data. Clicking on these functions links the user to a sub-page to carry out the functionality.

For example, FIGURE 7 shows an exemplary screen of a page under the add person and assign roles function. In this example, only persons with the following roles may be authorized to perform the add person and assign role functions: program manager, process coach, surrogate, coordinator. The authority to add persons and assign roles may be given by granting update authority to the persons with these roles by the senior executive.

In general, the ability to perform a function depends on the role of the person and whether that person has update authority granted by the senior executive. If given update authority, a program manager may add and update projects and account data for business units, add surrogates, set update authority within their domain, and view project progress for all business units. With update

authority, a process coach generally may add surrogates, set update authority, and view project progress for all business units. A surrogate with update authority may generally add and update projects and accounts for all business units under the respective program manager, and view project progress for all business units. A coordinator with update authority may add people, assign roles, add projects and accounts for business units in a defined scope. Account managers, if granted update authority, may generally update data for accounts and projects for which they are assigned responsibility and was given authorization to do so by the program manager. A project manager with update authority may update project data for which they are assigned a role, if authorized by the program manager. A business manager or technical architect may view projects in which they are assigned a role.

FIGURE 7 provides a list of persons in the project with the assigned roles for each person. It may be seen that certain persons have more than one assigned role. For example, Ann Blue is both a project manager and a technical architect for a business unit under the oversight of John Smith, as well as a technical architect for a business unit under the oversight of Bob Smith. Sam Jones serves the role of project manager, technical architect, and program coordinator for several business units.

FIGURE 8 is an exemplary screen of a web page to add a person to the system. Several data fields are provided to request relevant data associated with the person to be added, such as name, address, phone numbers, E-mail addresses, user identifier, etc. Persons are authorized to add persons and assign roles for subordinate role holders. For example, a program manager can add a coordinator. Also, each may add people and roles only if authorized by senior management. The permission to update is given by

setting an update authority flag associated with the people with the proper roles defined within the business unit.

FIGURE 9 is an exemplary screen of a web page to assign a new role to a person already defined in the system. Only program managers, process coaches, surrogates, and coordinators may be authorized to assign roles. In the Assign Person column, each data field has a drop-down list of names defined for the business units for which the requestor has edit capability. In the Business Unit column, again the business unit the person belongs to can be selected from the drop-down list of defined business units. This business unit list is limited to those on behalf of whom the requestor is authorized to act. Only those persons already added and defined for the specific business unit appear in the Assign Person drop-down list. The pull-down lists of roles only display those roles that the current user is authorized to assign, typically only those roles that are below the role of the user in the role hierarchy. Further, the pull-down list of business units only contains those business units on behalf of which the user is authorized to act as authorized by the user's role and update authority. Therefore, if the update authority flag associated with the user is not on or affirmative, then these pull-down lists will be empty.

FIGURE 10 is an exemplary screen of a web page providing update authorization to the personnel. Only a person having sufficiently high seniority or a role high in the role hierarchy, such as a program manager, may be authorized to update authorizations. This person will be required to accept responsibility and accountability for the senior executive to act on behalf thereof. Therefore, this screen is off-limits and inaccessible to most people on the team. Two authorization permissions are shown, update authority and surrogate. As described above, a surrogate may act for a senior level manager such as a

program manager. Therefore, the surrogate would have security clearance to access and change most of the data in program office database 12. However, even a surrogate would not have the authority to change the update authority of the personnel. Update authority would give the assigned person the ability to not only access the data but also to update or change it. However, the level of data the assigned person may update depends on the role of the person. For example, a project manager may only update project level data for which they are managers, and an account manager may only update account level data.

FIGURE 11 is an exemplary screen of a web page to add an account according to the present invention. Data fields are provided for the user to provide the account name, identify the account manager and coordinator, and the country. The pull-down list for each data field only contains those data items related to the business unit identified by the role and person identifier of the user. For example, the account manager pull-down list only contains names of those persons having an account manager role in the business units for which the user is authorized to act (as defined by his/her role and update authority). Examples of those roles that may be authorized with update authority to add accounts are program manager, process coach, surrogates, and coordinator. Further, the start date and end date fields for the account are provided. Other information associated with the account may also be requested. A similar web page may be provided to revise data associated with an existing account.

FIGURE 12 is an exemplary screen of a web page to update account forecast. This screen may be automatically displayed after the account is added. Using this page, a gross forecast amount for each category may be entered at the top, which is then automatically distributed evenly throughout the months between the start and end dates

entered previously for the account. Alternatively, forecast amounts by month for the account may be entered. Because the program shown in the screen shot is a year 2000 remediation program, the forecasts amounts are associated with Y2K and non-Y2K revenues and expenses.

If an actual start date was identified, a web page for the entry of monthly actual amounts is automatically displayed, an example of which is shown in FIGURE 13. The user may then enter the monthly actual revenue and expense amounts.

Account forecast data may be revised or updated by program managers, process coaches, surrogates, and coordinators. Account actual amounts may also be updated on a periodic basis to report account-level financial information. An exemplary screen for account actual update is shown in FIGURE 14. Periodic account actual updates capture useful information for reporting to the senior executives and board of directors of the organization. Because account actual information is typically available at a lower level in the chain of command, account actual updates may be entered by project managers and account managers, as well as program managers, process coaches, surrogates, and coordinators. In the embodiment shown, monthly updates are required.

In order to more easily determine that monthly updates of account actuals are entered, the concept of a worklist is used. A worklist is a list of all the data that still remain to be updated at a given time. At the beginning of each reporting or update period, the worklist contains the entire list of data that are required for a project for that period as well as for any previous period, if they were not updated previously. As data are entered by each account manager, that data entry is removed from the worklist. Therefore, a project manager or any one having a management role is able to, at one glance, determine

which data still need to be updated each month or each period. In the update account actuals screen shown in FIGURE 14, a 0\$ column may be checked if no data is to be reported for that month, so that the worklist may be modified with the month's actual removed. In other screens, the option of checking off a no change (N/C) box also functions to remove that particular data from the worklist. In this manner, affirmative action is required to remove a data from the worklist, either by providing update data or by indicating that no change or progress has been made in that time period.

FIGURES 15-17 provide exemplary screens for adding, revising, and updating project information. FIGURES 15A and 15B are an exemplary screen for adding a new project to an account. Only persons with certain assigned roles such as program manager, process coach, surrogate, and coordinator may have authorization to add projects. After selecting the business unit from a drop-down list, the screen shown in FIGURES 15A and 15B appears for the user to enter data associated with the project to be added. The project name, project code are entered. The project manager field, business manager field, coordinator field, and technical architect/owner field each has a drop-down list of possible names of persons who may fulfill these roles for this project. In this manner, data entry is very controlled and therefore errors are largely minimized or eliminated. Project must start date and project failure dates are then entered in the appropriate fields. From the tactic drop-down list, the appropriate tactic is selected. From the selected tactic, milestones are determined.

In the next section, Impacting Program, those programs that fund the project wholly or partially are selected. If the project is fully funded by one program, 100% is entered by the appropriate program, otherwise, those programs that share the project are selected with the appropriate

percentage funding entered. Further, the program that own the project is selected, and those programs that may impact the progress of the project are also selected.

5 In the next section, the number of units for the primary work components of the project and how much labor percentage is allocated to each component are entered. Work components may be lines of code, hardware equipment or devices, network components, etc.

10 In the next section, the estimated annualized contingency costs that will be incurred if the project fails or is not approved is entered. Once information on this screen is fully entered, selecting the next button prompts the second add project screen to be displayed, as shown in FIGURE 15C. From the drop-down lists, select the
15 appropriate functional area, country, and weight impact information. The next screen is shown in FIGURE 15D, which prompts for project milestone data. The milestones are determined by the previously selected tactic. The milestones may be user-defined so that users can add
20 tactics to identify their own set of milestones. Alternatively, the end user may utilize industry standard tactics and milestones. Target start date, actual start date, target end date, actual end date, and percent completed data are entered for each milestone.

25 In FIGURE 15E, an exemplary screen for entering project forecast data is shown. The monthly forecast amounts may be entered or a gross amount may be entered at the top, which will be distributed evenly throughout the months. The forecast amounts are entered for hardware
30 costs, software costs, labor costs, and full time equivalents (FTEs).

If an actual start date were entered on the milestone screen in FIGURE 15D, then a project actual screen appears. An exemplary project actual screen is shown in FIGURE 15F.

The project actual amounts may be entered in the appropriate columns.

The project data and forecasts may be revised. The basic information associated with the project, such as people assigned, may be revised as well as re-baseline project dates and costs. For example, target and actual start and end dates for the milestones may be revised or updated; the hardware, software and labor cost forecasts may be revised or updated; and the hardware, software and labor cost budgets may be revised or updated. Old baseline information are archived as project history in program office database 12. The manner in which project history is stored is described below. Further, the impacting program, work component, contingency cost, and weight information of the project may also be revised or updated via appropriate screens (not shown).

As described above, web user interface 15 may be used to periodically update the actual amounts or values for budget, labor, schedules, and progress. Budget and labor actuals may be periodically updated by a program manager, process coach, surrogate, or an account manager. FIGURE 16 shows an exemplary screen for entering budget and labor actuals. If the project did not consume cost or FTEs for the period, checking the 0\$ box removes that item from the worklist for the period.

Project schedules and progress actuals may also be updated periodically. An exemplary screen for updating schedules and progress actuals is shown in FIGURE 17. This screen contains an entry for each project in the account or program that has an incomplete milestone. Only program managers, process coaches, surrogates, and coordinators may have access to this screen. The percent completed field may be updated to show progress toward a milestone that has not reached the end date. This percent completed data is determined independent of the forecasts or actuals in terms

of labor resources or dollar amounts. The N/C boxes may be checked to indicate that the data for the milestone is unchanged for the reporting period or no progress has been made during the reporting period. This action removes the item from the worklist so that the program office is able to distinguish projects that are not being updated from those that are stalled or in trouble.

FIGURES 18-20 are exemplary screens of self-extracting user interface 16 to allow users to report periodic update data. Self-extracting user interface 16 is primarily intended to be used by account managers to report account-level data to upper management.

FIGURE 18 is the first screen that is displayed when self-extracting user interface 16 is executed. As shown, several account and project functions are available, such as view or review account and project basic data, view or review account and project forecasts, update account actuals, update budget and labor actuals, update schedule and progress actuals. These functions are displayed on buttons which may be clicked on to initiate the respective function. These functions are similar or the same as those described above to provide updates or revisions to account and project data. However, because self-extracting user interface 16 is not browser-based, the screens and the manner in which the data are entered may be different. For example, if self-extracting user interface 16 is based on a spread sheet program such as Microsoft Excel, then the data fields are likely to be displayed and entered in a spread sheet format.

FIGURE 19 is an exemplary screen or view to revise account forecast data using self-extracting user interface 16. Note that the cells may be coded or colored according to the status of the data contained therein. In this manner, cells that have not been updated, cells containing erroneous data, and cells containing valid data are flagged

to the user to take appropriate action, if needed. For example, in the results column, cells that still need update data may be coded blue, cells that contain data that seem suspicious or questionable may be coded yellow (as compared with some predetermined criteria or range), cells that contain erroneous data may be coded red, and cells that contain data that is neither suspicious or erroneous may be coded green. Therefore at one glance, the user is able to direct his or her attention to those data items that require additional verification or input.

FIGURE 20 is an exemplary screen to update account actuals using self-extracting user interface 16. This screen displays an additional feature, the ability to toggle between the worklist and the entire list. As described above, the worklist is a list of those data items that require periodic update. As data items are entered or updated, they are removed from the worklist, so that only those data items still requiring input at any one point are displayed. At the end of the reporting period when a coordinator or program manager views the worklist, it should be empty, indicating that all data requiring update have been updated in a timely manner. The screens for updating account actuals, budget and labor actuals, and schedule and progress actuals preferably have this toggle option to either view only the data items in the worklist or all data, with the ability to quickly toggle between these two views.

Referring to FIGURES 21 and 22, two views of an exemplary relational data model of the data structure used in the system and method of managing a program office of the present invention are shown. Each data table and selected data fields contained therein are described below as well as the relationships between the data tables and data fields.

The account table 100 stores attributes unique to an account and current values of dependent parameters. The account identifier is the primary key of the table, which uniquely identifies the account. The account table further contains a business unit identifier (BUID), which may be the personal identifier of the executive who has oversight responsibility over the business unit. The account name, name of the account manager are also provided in the account table.

The account table 100 is linked to the account actual table 102 and the account forecast table 104 by the account identifier. The account table 100, account actual table 102 and the account forecast table 104 are used in this embodiment to track those accounts in which the expenses are offset by the revenues. The account actual table stores the actual amounts of the account by the reporting period, such as monthly reporting. Revenue and expense actual amounts are stored in the account actual table 102. In the embodiment shown, revenues and expenses associated with the Y2K account are stored, but such data fields may be generalized or customized for other types of projects. The account actual table 102 may include non-Y2K revenues, non-Y2K expenses, Y2K revenues, and Y2K non-project expenses.

Similarly, the account forecast table 104 stores revenue and expense budgets for the account for each reporting period. The account forecast table 104 may include non-Y2K revenue budget, non-Y2K expense budget, Y2K revenue budget, and Y2K non-project expense budget.

A person table 106 stores the attributes related to each person referenced with a role in program office database 12. The person identifier is the primary key in this table. Attributes in the person table may include the person's name, user identifier, password, and all relevant contact information.

The person table 106 is linked to an assignment table 110, a role table 112, and a surrogate table 114 by the person identifier. The assignment table 110 lists persons who are allowed to fill certain roles for specific business units. The assignment table 110 also contains the business unit identifier which identifies the business unit that the assignments are valid for. The role data field contains the assigned roles for the business unit. The update authority data field contains person identifiers of those persons having the authority to update or change the data associated with data of that business unit.

In the role table 112, the role data field is a primary key. Description of each role is defined (RoleDescrip) and the hierarchical authorization level of each role (RoleLevel) are defined. In the surrogate table 114, the person identifier again is the primary key along with a surrogate identifier. The surrogate identifier is the person identifier of the person assigned as the surrogate for the senior executive for the business unit. Additionally, a surrogate add date for the date the surrogate status was assigned to the person and a surrogate delete date field for the date the surrogate status was taken away are stored in the surrogate table.

Data tables related to projects include a project table 120, which stores attributes unique to a project and current values of dependent parameters of the project. Project attributes include those that are required, those that are used for audit purposes, those that are program objective specific, and those that are optional. Required attributes include a project identifier (ProjectID) which uniquely identifies each project. Project Name stores the name of the project. Active indicates the current status of the project. The Tactic field identifies the tactic defined for the project. The business unit to which the project belongs to are also identified with the business

identifier (BUID). Audit attributes may include data items such as Project Plan, which provides the plan for the project; Doable, which indicates whether the project can be completed with the project plan; Team, which identifies the team personnel; On Schedule, which indicates whether the project is on schedule with respect to the milestones; and approval level, which indicates whether the project is approved and pending or inactive, and further how to account for the dollars spent in a project that is now inactive. The audit attributes can only be updated or changed via program office interface 13 by auditors.

Other attributes are program objective specific which may change according to the needs of the program. Program objective specific attributes may include Mission Critical, which indicates whether the completion of the project is critical to the success of the corporation; Functional Area, which identifies areas covered by the project such as human resources, infrastructure, accounting, purchasing, customer services, etc.; and Country, which indicates the geographical location of the project. Other program objective specific attributes may include those that identify the coordinator, project manager, technical architect, and business manager that have oversight responsibility over the project (Coordinator, ProjMgr, TechArch, BusMgr). Previously described date values, the must start date of the project (MustStartDate) and failure date (ProjectFailureDate) of the project are also stored in project table 120. The remainder may be optional attributes. It is important to note that the attributes, aside from the required attributes, may be modified to tailor the type of project and what aspects of the project are crucial to monitor and report.

The project table 120 is linked by the project identifier to many other data tables, including the project forecast table 122, project forecast history table 124,

project actual table 126, milestone actual table 128, milestone forecast table 130, milestone forecast history table 132, transaction log table (TransLog) 134, project and program cross-reference table 136, and project roadblock table 138. Because the project forecast table 122, the project actual table 126, and the project forecast history table 124 contain financial information, access to data stored in these tables is strictly guarded to allow only personnel with the appropriate role and authorization level to view the information.

The project forecast table 122 contains the current budget forecast amounts for the project. The project identifier and the month are primary keys for this table. The hardware, software, labor and other budget amounts entered and updated via web user interface 15 and self-extracting user interface 16 are stored here.

The project forecast history table 124 stores the original budget forecasts when the current forecasts stored in the project forecast table 122 are different from the original. Therefore, the project forecast history table 124 may be null when the original budget forecast amounts have not been changed. This archive scheme means that the project budget forecast amounts are only stored in the project forecast history table 124 only when a change has been made and not done on a periodic basis.

The project actual table 126 contains the actual project dependent values reported periodically. The project identifier and the month the expenses were incurred are the primary keys. The data fields include the actual expenses used on hardware, software, labor, etc.

The milestone forecast table 130 maintains the current forecasted milestone dates. If no changes have been made to the original forecasts, then the current forecast is also the original forecast. The project identifier and the milestone are the primary keys to the table. The target

milestone start date and end date, and the actual milestone start date and end date are stored in this table.

The milestone forecast history table 132 maintains the first or original forecast if changes have been made to the original forecast. Therefore, if no changes have been made to the original forecast, then this table would be empty. If the forecast has been changed more than one time, the milestone forecast history table 132 will still maintain the original forecast, and forecasts other than the original and the current forecasts are stored and archived in the TransLog table. The project identifier and the milestone are the primary keys to the table. The target milestone start and end dates are archived in this table.

In the milestone actual table 128, the project identifier, milestone, and the reporting period are the primary keys. This table maintains the actual percentage completed (PctCompl) or progress toward the milestone during the respective reporting period. In addition, a MSActUpd attribute is a flag that indicates whether project milestone actual dates or percent complete were updates, or whether the user indicates there is no change in progress for the period.

The transaction log table 134 stores pertinent data associated with changes to program office database 12, such as the project identifier of the project affected, person identifier of the person making the change, and date and time of the transaction (TransTS). These are the primary keys to the table. Data fields include the transaction type, the transaction SQL (TransSQL), the name of the table changed, and the number of days to maintain the transaction log entry (KeepDays). Recall that project forecast table 122 maintains the current forecast and the project forecast history table 124 maintains the original forecast. Anything changes made between the original forecast and the current forecast are recorded in the transaction log table

5

15

25

30

program is under the control of the program office, so that financial data should be collected.

Another data table, UserWeight 140, stores the business unit weighting data of systems required for the business units to deliver value to the company. As described above, value to the company may be measured empirically in terms of revenue, earnings and profit, but value can also be determined by user weights stored in this table. As described above, user weights may be entered via user interfaces 15 and 16 using a screen similar to that shown in FIGURE 15C, for example. In this manner, projects may be prioritized based on empirical value or value judgments in terms of the systems the projects affect, and how important these systems are to the business units.

The work component table 142 lists the valid work component categories. The work component name (WCName) is used as the primary key. The data field, WCUnt, is the type of work component, such as lines of code, hardware device, network device, facilities, etc. The data field, WCDescrip, provides further description of the work component.

The work component table 142 is linked to the project table 120 or project identifier by the project work component cross-reference (ProjWCXref) table 144. The work component table 142 stores the amount and type of work covered in a project. This table uses the project identifier and work component name as primary keys to access the work component count (WCCount) and the work component percentage (WCPct). WCCount is the count of the work component, and WCPct is the labor effort percentage required for the respective project.

The project is linked to the system by the SysProjXref table 146, which uses the project identifier and the system identifier to link the tables associated with projects to the tables associated with systems. A system table 148 is

accessed using the system identifier as the primary key and contains the system name, system description, and an indicator of whether the system is currently active.

The next set of data tables is primarily responsible for the project management methodology independence of the present invention. A tactic table 150 has tactic as the primary key. The tactic is entered or selected for the project as described above when the project is added to the database. The tactic is used as a primary key in the tactic table. Other data fields include tactic type, tactic owner, and tactic description. Tactic type provides categories of valid tactic types. Tactic owner is the identifier of the person who defined the tactic as well as the milestones within the tactic. As part of defining the tactic, the tactic owner also specifies the milestone categories for the milestones, and the tactic type for the tactic. Tactic description provides a description of the tactic.

The tactic type table 152 is linked to the tactic table 150 and lists the categories of valid tactic types used for referential integrity. The tactic type is the primary key. Tactic type description provides description of the tactic types.

The tactic milestone (TacticMS) table 154 is linked to the tactic table 150 and stores the cross-reference information between milestones and tactics. The tactic milestone table 154 shows which milestones are used for which tactics. The tactic and milestone fields are primary keys to this table. MSCat is a data field that stores the milestone categories. MSDescrip is a data field that stores the description of each milestone.

The MSCat table 156 is a table that stores milestone categories. The milestone category is the primary key. Milestone categories may include assess, renovate, test and implement. Data fields include the milestone category

description (MSCatDescrip) and a milestone category sort control field (MSCatSort).

The TTypeMSCatXref table 158 stores the cross-reference information on which milestone categories are required for which tactic types. Tactic type and milestone category are primary keys in this table. Using this table, milestones defined in a pre-existing project defined or managed in another project management tool may be cross-referenced or mapped to the defined tactic types of the present program office management system and methodology. Accordingly, a project managed by a conventional project management methodology or tool with its own set of milestones may be translated to the tactic types of the present system. In this manner, the project may be continued to be managed with the previous methodology or tool but reporting of that project's progress may be made in terms of milestone categories or common terms as described in the present invention.

Some additional data tables round out the functionality of program office database 12. The country table 160 provides a specification of the geographical location of the project. The business unit table 162 maintains attributes for reach business unit defined in the system and is accessed by the business unit identifier. The senior executive table 164 lists the senior executives in the company who are also assigned priority by an executive weighting scheme. The business unit program leader table (BUPgmLdr) 166 lists the program leaders for each business unit, such as the executive sponsor, program manager, and process coach.

Using these relational data tables in program office database 12, logical views or reports may be generated easily to provide information to upper management so that intelligent strategic decisions may be made with respect to

656030"0544260

all projects and programs undertaken by the corporation and across multiple geographical boundaries.

FIGURES 23-30 are exemplary screens of program office interface 13 for managing a Year 2000 program office. A number of functions are provided, including update project data, project detail report, update account data, account detail report, tech team functions, people and assignments, archive, CSRs, and create Excel tool extract.

FIGURE 24 is an exemplary screen to select a project. When one or more of the criteria are selected by the pull down lists, those projects satisfying the selected criteria are shown by clicking on the Show Projects button.

FIGURE 25 is an exemplary screen to display some basic information as well as audit data about a project, including the project identifier, country, functional area, project name, tactic, active status, approval level, project plan, doable, on schedule, project remove date, mission critical flag, business unit identifier, account identifier, and identity of the coordinator, technical architect, project manager, and business manager, etc. A series of buttons may be clicked on to display additional update information, such as the project forecasts, project actuals, milestone dates, milestone progress, and project programs.

FIGURE 26 is an exemplary screen to display project forecasts in program office interface 13. FIGURE 27 is an exemplary screen to display milestone dates. FIGURE 28 is an exemplary screen to display milestone actuals. FIGURE 29 is an exemplary screen to display project program cross references including the percentage ownership data. FIGURE 30 is an exemplary screen to create project detail report. Ad hoc reports may be easily created by using SQL queries on the data fields of the data tables shown in FIGURE 21.

The program office management system and method of the present invention provide many strategic advantages. One

advantage is the ability to monitor projects managed under non-identical project management methodologies and data sources. Milestones unique to particular projects may be translated to industry standard milestones used in the present invention. Organizational costs, schedules and resources can be managed and controlled across the organization on many levels. Further, access to system data is securely and strictly controlled based on a user's identifier, the user's role(s), and authorization levels. Yet another advantage of the present invention is the ability to archive project history with minimal data storage. Priority in terms of empirical figures and value judgment weights can be assigned to projects in the entire organization to intelligently allocate resources.

It may be advantageous to note that the nomenclature of the detailed description is represented largely in terms of processes and symbolic representations of operations by conventional computer components, such as a central processing unit ("CPU") or processor associated with a general purpose computer system, memory storage devices for the processor, and connected pixel-oriented display devices. These operations include the manipulation of data bits by the processor and the maintenance of these bits within data structures resident in one or more of the memory storage devices. Such data structures impose a physical organization upon the collection of data bits stored within computer memory and represent specific electrical or magnetic elements. These symbolic representations are the means used by those skilled in the art of computer programming and computer construction to most effectively convey teachings and discoveries to others skilled in the art.

For the purposes of this detailed description, a process, method, routine, or sub-routine is generally considered to be a sequence of computer-executed steps

leading to a desired result. These steps generally require manipulations of physical quantities. Usually, although not necessarily, these quantities take the form of electrical, magnetic, or optical signals capable of being stored, transferred, combined, compared, or otherwise manipulated. It is conventional for those skilled in the art to refer to these signals as bits, values, elements, symbols, characters, texts, terms, numbers, records, files, or the like. It should be kept in mind, however, that these and some other terms should be associated with appropriate physical quantities for computer operations, and that these terms are merely conventional labels applied to physical quantities that exist within and during operation of the computer.

It should also be understood that manipulations within the computer are often referred to in terms such as adding, comparing, moving, or the like, which are often associated with manual operations performed by a human operator. It must be understood that no involvement of the human operator may be necessary, or even desirable, in the present invention. The operations described herein are machine operations performed in conjunction with the human operator or user that interacts with the computer or computers.

In addition, it should be understood that the programs, processes, methods, and the like, described herein are but an example of one implementation of the present invention and are not related or limited to any particular computer, apparatus, or computer language. Rather, various types of general purpose computing machines or devices may be used with programs constructed in accordance with the teachings described herein. Similarly, it may prove advantageous to construct a specialized apparatus to perform the method steps described herein by way of dedicated computer systems with hardwired logic or

programs stored in non-volatile memory, such as read only memory (ROM).

5 Although several embodiments of the present invention and its advantages have been described in detail, it should be understood that mutations, changes, substitutions, transformations, modifications, variations, and alterations can be made therein without departing from the teachings of the present invention, the spirit and scope of the invention being set forth by the appended claims.

66E020" 05544360

WHAT IS CLAIMED IS:

1. A program office management system, comprising:
a program office database storing:

informational data associated with accounts,
projects, and programs;

financial data associated with the accounts,
projects, and programs;

schedule and progress data associated with
the accounts, projects, and programs;

data associated with personnel, roles, and
security access information thereof;

data associated with translating progress
milestones; and

update data associated with the progress,
actual expenditures, and labor resources of the
projects and programs;

at least one user interface operable to display data
stored in the program office according to a predetermined
security scheme based on the security access information
stored in the program office database, and further operable
to receive the update data on a periodic basis.

2. The system, as set forth in claim 1, wherein the
program office database comprises a plurality of relational
data structures.

3. The system, as set forth in claim 1, wherein the
at least one user interface comprises at least one web-
based user interface.

4. The system, as set forth in claim 1, wherein the
at least one user interface comprises at least one self-
extracting executable user interface.

5. The system, as set forth in claim 1, wherein the at least one user interface comprises at least one program office interface.

5 6. The system, as set forth in claim 1, wherein the program office database comprises more than one copy of the data residing in more than one distributed databases.

10 7. The system, as set forth in claim 1, wherein the user interface comprises more than one copy of the user interface residing in more than one distributed computing system.

15 8. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise an assignment table associating a person to at least one role defined within a business unit.

20 9. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise an assignment table associating a person to at least one role defined within a business unit, and further to at least one predefined update authority level set by a person having a senior management role within the
25 business unit.

30 10. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise definitions of an hierarchy of roles having increasing degrees of access and functionality to the data in the program office database.

64-99-001-0554260

11. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise a role definition of a program manager having authorization to view and change all project and account data associated with at least one business unit, and to view and change all personnel data associated with persons assigned to the at least one business unit.

12. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise a role definition of a coordinator having authorization to assign one or more persons to the at least one business unit, assign at least one role to each person, and add projects and accounts for the at least one business unit.

13. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise a role definition of an account manager capable of having authorization to update account data and project data.

14. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise a role definition of a project manager capable of having authorization to update project data.

15. The system, as set forth in claim 1, wherein the data associated with security access information of personnel comprise a role table operable to store at least one valid role and an authorization hierarchical organization of the at least one valid role.

16. The system, as set forth in claim 1, wherein the data associated with translating progress milestones comprise a data table operable to map milestones predefined in a project to milestone categories predefined within the program office database.

17. The system, as set forth in claim 1, wherein the data associated with translating progress milestones to tactics comprise:

a tactic table operable to store at least one predefined tactic supported by the program office database and a tactic type for each tactic; and

a tactic type to milestone category cross-reference table operable to map the at least one milestone category to the at least one tactic type.

18. The system, as set forth in claim 1, wherein the financial data comprise:

a project forecast table operable to store at least one current budget forecast amount for the project; and

a project forecast history table operable to store an original budget forecast amount if it is different than the at least one current budget forecast amount.

19. The system, as set forth in claim 1, wherein the financial data comprise:

an account forecast table operable to store at least one revenue and expense budget amount associated with an account; and

an account actual table operable to store at least one revenue and expense actual amount associated with the account.

20. The system, as set forth in claim 1, wherein the informational data comprise a project table operable to store informational data associated with at least one project identified by a project identifier.

5

21. The system, as set forth in claim 20, wherein the project table comprises:

a project identifier uniquely identifying each project;

10

a business unit identifier of a business unit to which the project belongs to;

at least one person identifier of a person assigned a role having a predetermined responsibility for the project; and

15

a status flag indicative of whether the project is active, pending, or inactive.

22. The system, as set forth in claim 1, wherein the information data include an account table comprising:

20

an account identifier uniquely identifying each account;

a business unit identifier of a business unit to which the account belongs to; and

25

a person identifier of a person assigned the role of an account manager for the account.

23. The system, as set forth in claim 1, wherein the schedule and progress data comprise a milestone actual table operable to store an amount of progress into a specific milestone for a given period for a project.

30

64-99-001-0544260

24. The system, as set forth in claim 1, wherein the schedule and progress data comprise:

a project identifier of a project;

a milestone defined for the project;

5 a reporting period; and

a percentage completion value of the milestone in the reporting period independent of forecast or actuals.

10 25. The system, as set forth in claim 1, wherein the update data comprise:

a project actual table operable to store actual expenditure amounts spent during a specific reporting period for a project; and

15 a milestone actual table operable to store a percentage completion value of a specific milestone defined for a project during the specific reporting period.

20 25. The system, as set forth in claim 24, wherein the update data further comprise an account actual table operable to store actual expenditure amounts spent during the specific reporting period for an account.

25 26. The system, as set forth in claim 1, wherein the program office database further comprises a user weight table operable to store a weight value indicative of importance for each system affected by the projects and programs.

30 27. The system, as set forth in claim 1, wherein the program office database further comprises a project roadblock table operable to store information about a problem encountered in a project identified by a project identifier and to enable escalated reporting to upper management about unresolved problems.

35

28. The system, as set forth in claim 27, wherein the project roadblock table comprises:

roadblock type;

date and time that the problem was encountered; and

data on how and when the problem was resolved.

29. The system, as set forth in claim 1, wherein the program office database further comprises a transaction log table operable to record what changes were made to data stored in the program office database, who made the changes, and when the changes were made.

30. The system, as set forth in claim 1, wherein the program office database comprises required data, audit data, program objective specific data, and optional data.

31. A method of managing a program office, comprising:

storing and accessing data associated with at least one project in a program office database, including informational data, financial data, schedule and progress data associated with the at least one project;

storing update data associated with the at least one project;

identifying persons associated with the at least one project, defining a role hierarchy having roles associated with increasing levels of data access, assigning at least one role relevant to the at least one project to each person, and storing data associated with the persons and their assigned roles in the program office database; and

mapping milestones defined in the at least one project to tactics defined in the program office database for reporting purposes.

10

15

20

25

30

35

38. The method, as set forth in claim 31, wherein assigning at least one role comprises assigning a role of project manager, a role capable having authority to update project data for a respective project.

5

39. The method, as set forth in claim 31, wherein storing and accessing data comprise storing and accessing data stored in at least one relational database.

10

40. The method, as set forth in claim 31, wherein storing and accessing data associated with the persons and their assigned roles comprise:

15

storing and accessing an assignment table associating a person identifier to at least one role defined within a specific business unit; and

granting at least one predefined update authority to the person identifier by a person having a predetermined upper management role.

20

41. The method, as set forth in claim 31, wherein storing and accessing data associated with the persons and their assigned roles comprise storing and accessing a role table having at least one valid role and an authorization hierarchical organization of the at least one valid role.

25

09244550-020399

5

storing and accessing a milestone category table
having at least one category of milestones; and

10

15

20

25

45. The method, as set forth in claim 31, wherein storing and accessing the financial data comprise:

storing and accessing an account forecast table operable to store at least one revenue and expense budget amount associated with an account; and

storing and accessing an account actual table operable to store at least one revenue and expense actual amount associated with the account.

46. The method, as set forth in claim 31, wherein storing and accessing the informational data comprise:

storing and accessing a project table operable to store informational data associated with at least one project identified by a project identifier; and

storing and accessing an account table operable to store informational data associated with at least one account identified by an account identifier.

47. The method, as set forth in claim 31, wherein storing and accessing the project table comprise:

storing a project identifier uniquely identifying each project and using the project identifier as a primary key to the project table;

storing and accessing a business unit identifier of a business unit to which the project belongs to;

storing and accessing a person identifier of a person assigned at least one role for the project; and

storing and accessing a status flag indicative of whether the project is active, pending, or inactive.

```

    storing and accessing an account identifier uniquely
    identifying each account;

```

storing and accessing a person identifier of a person assigned the role of an account manager for the account.

50. The method, as set forth in claim 31, wherein storing and accessing the schedule and progress data comprise:

```
    storing and accessing a milestone defined for the
project;
```

storing and accessing a reporting period; and
storing and accessing a percentage completion value of
the milestone in the reporting period.

storing and accessing a project actual table having actual expenditure amounts spent during a specific reporting period for a project; and

storing and accessing a milestone actual table having a percentage completion value of a specific milestone defined for a project during the specific reporting period.

52. The method, as set forth in claim 51, wherein storing and accessing the update data further comprise storing and accessing an account actual table having actual expenditure amounts spent during the specific reporting period for an account.

53. The method, as set forth in claim 31, further comprising storing and accessing a user weight table having a weight value indicative of importance for each system affected by the projects and programs.

54. The method, as set forth in claim 31, further comprising:

storing and accessing a project roadblock table having information about a problem encountered in a project identified by a project identifier; and

reporting any problem to management unresolved after a predetermined time period.

55. The method, as set forth in claim 54, wherein storing and accessing the project roadblock table comprise:

storing and accessing a roadblock type;

storing and accessing a date and time that the problem was encountered; and

storing and accessing data on how and when the problem was resolved.

56. The method, as set forth in claim 31, further comprising storing and accessing a transaction log table having what changes were made to data stored in the program office database, who made the changes, and when the changes where made.

57. The method, as set forth in claim 32, wherein storing and accessing the data comprise storing and accessing data via a web browser-based user interface implementing a security scheme using the role and update authorization level assignment to the users.

58. The method, as set forth in claim 32, wherein storing and accessing update data comprise storing the update data via a self-extracting spread sheet-based user interface implementing a security scheme using the role and update authorization level assignment to the users.

59. The method, as set forth in claim 31, further comprising:

retrieving data from at least one other data source; and

verifying data in the program office database with the data from the at least one other data source.

60. The method, as set forth in claim 31, further comprising:

retrieving data from at least one project management tool; and

using the data from the at least one project management tool in views, reports, and audits.

61. The method, as set forth in claim 31, further comprising:

retrieving data from at least one project management tool; and

storing the data from the at least one project management tool in the program office database.

62. A system for managing at least one program including a plurality of projects, comprising:

at least one program office database storing:

informational data associated with projects

5 and programs;

financial data associated with the projects, and programs;

schedule and progress data associated with the projects, and programs;

10 personnel data associated with persons having responsibility associated with the projects and programs, the personnel data including a unique person identifier for each person;

15 security data having an assignment of at least one role to each person and an assignment of at least one update authorization to certain persons having oversight responsibility;

20 data associated with translating progress milestones defined in the projects to tactics defined in the system; and

update data associated with the progress, actual expenditures, and labor resources of the projects and programs;

25 at least one user interface operable to display and allow access to the data stored in the program office according to a predetermined security scheme based on the person identifier, role and update authorization assignment stored in the at least one program office database, and
30 further operable to receive the update data on a periodic basis.

034450-00399

A system and method for managing at least one program including a plurality of projects for at least one organizational unit are provided. The system includes at least one program office database which stores:

10

15

20

25

update data associated with the progress and actual expenditures of the accounts, projects, and programs;

30

35

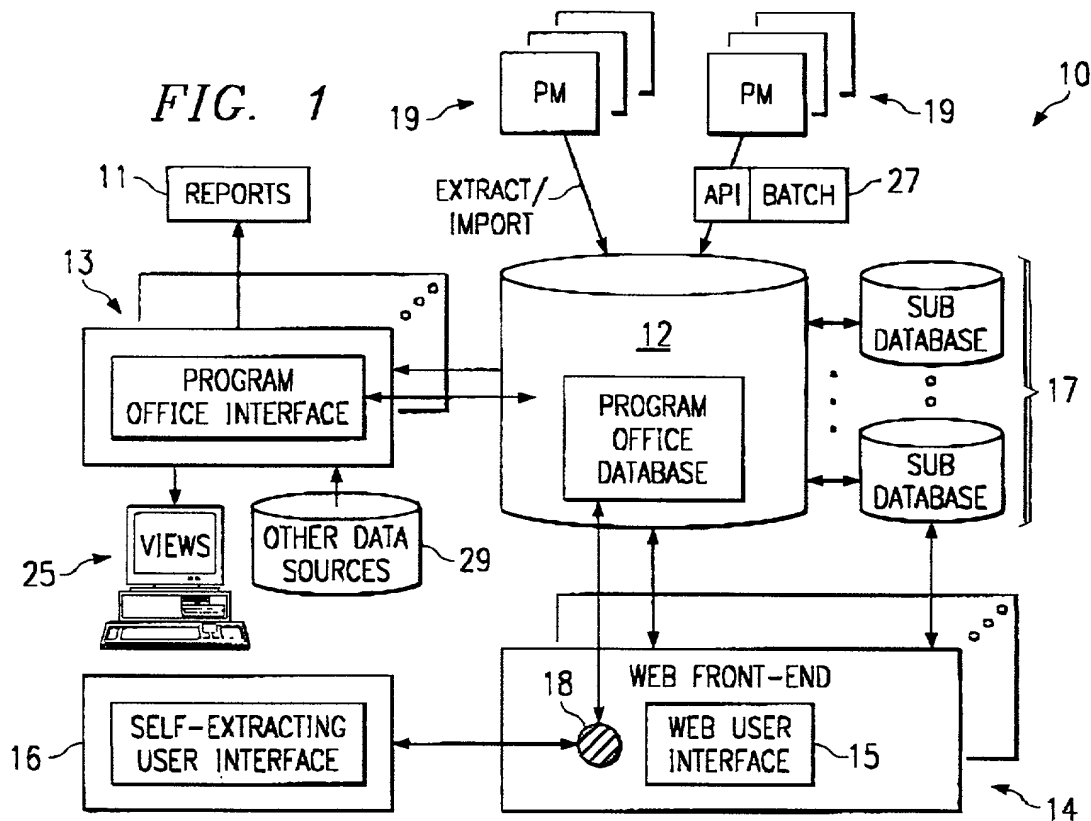


FIG. 2

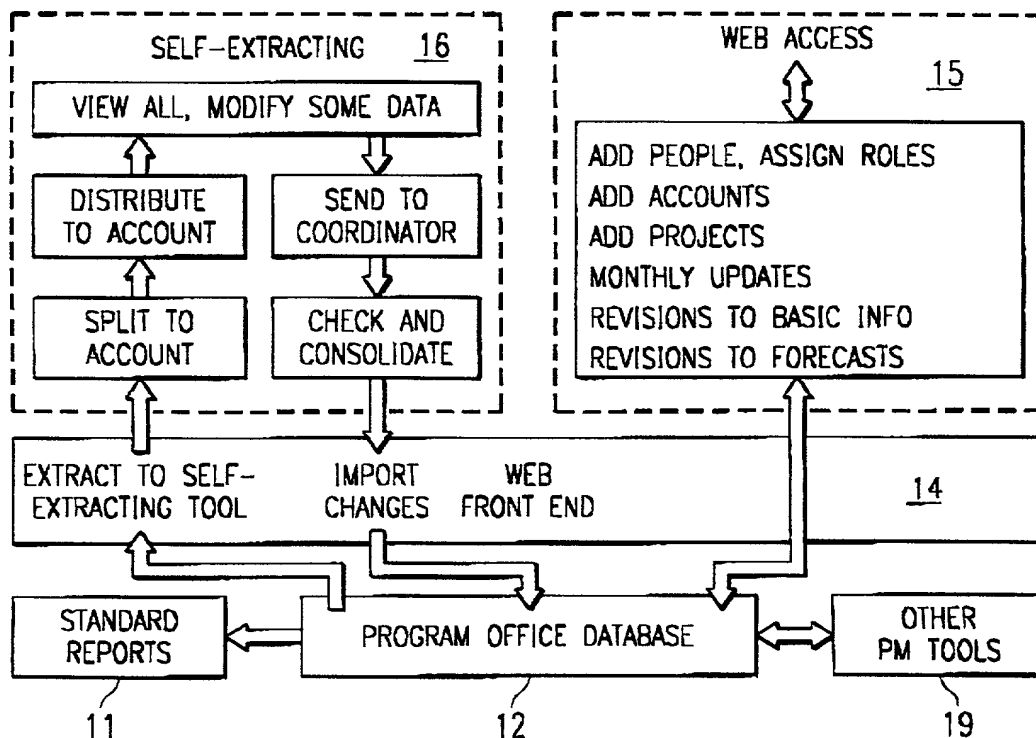


FIG. 3

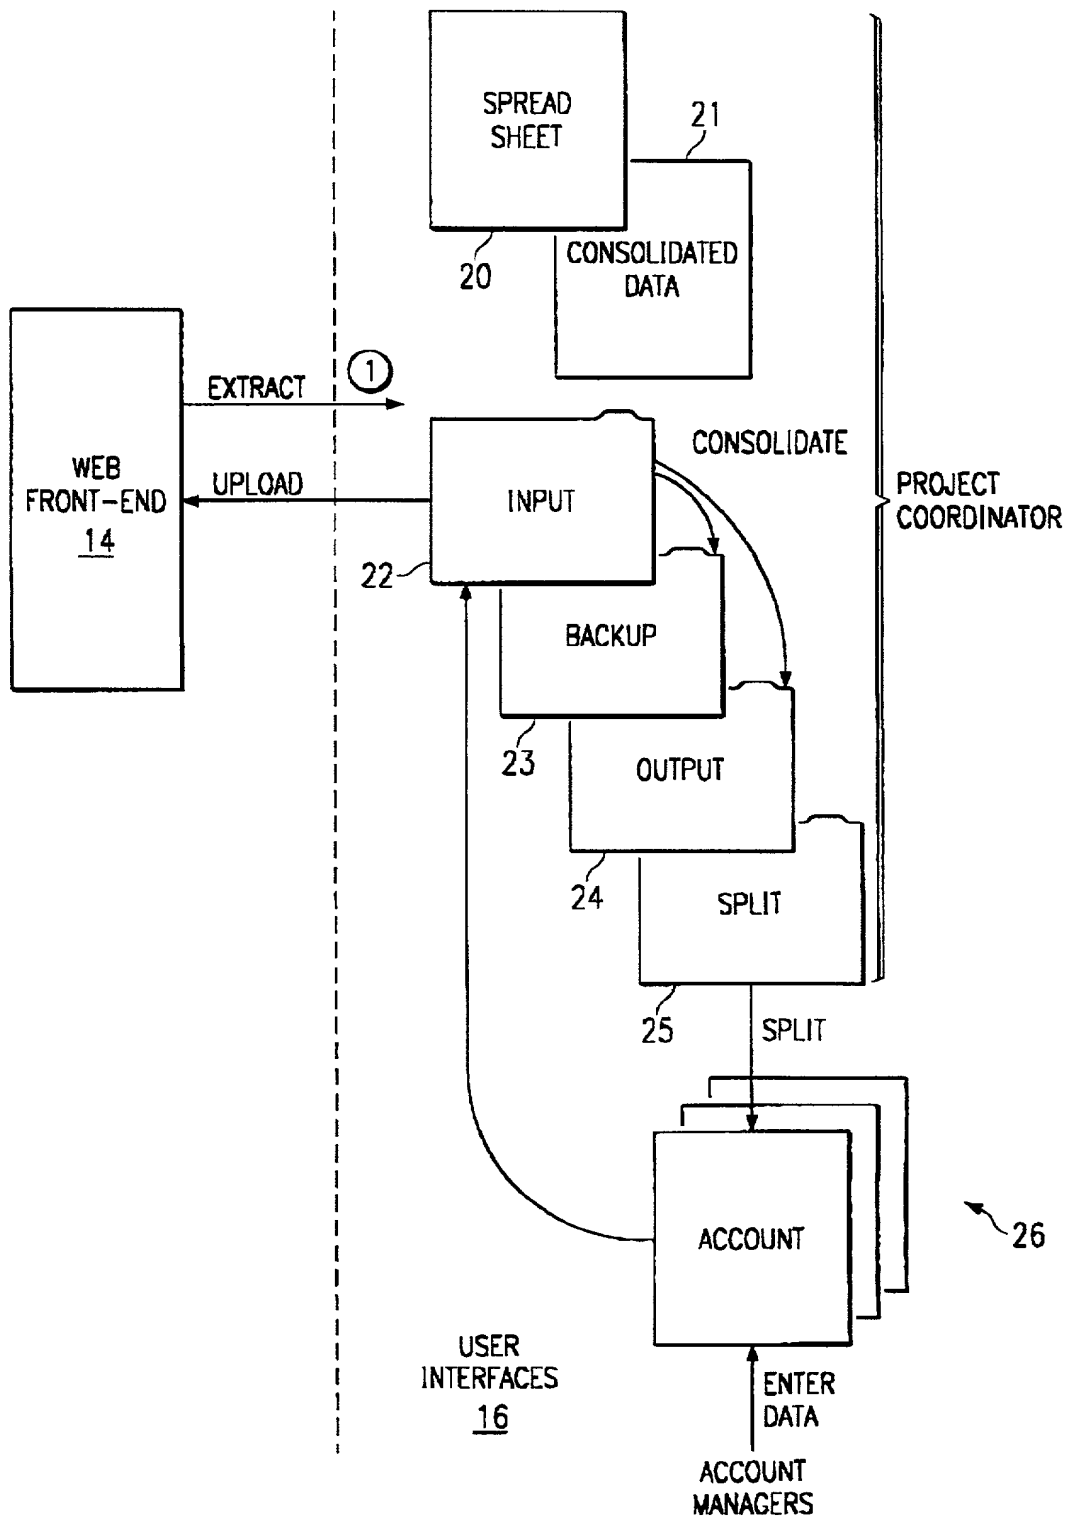
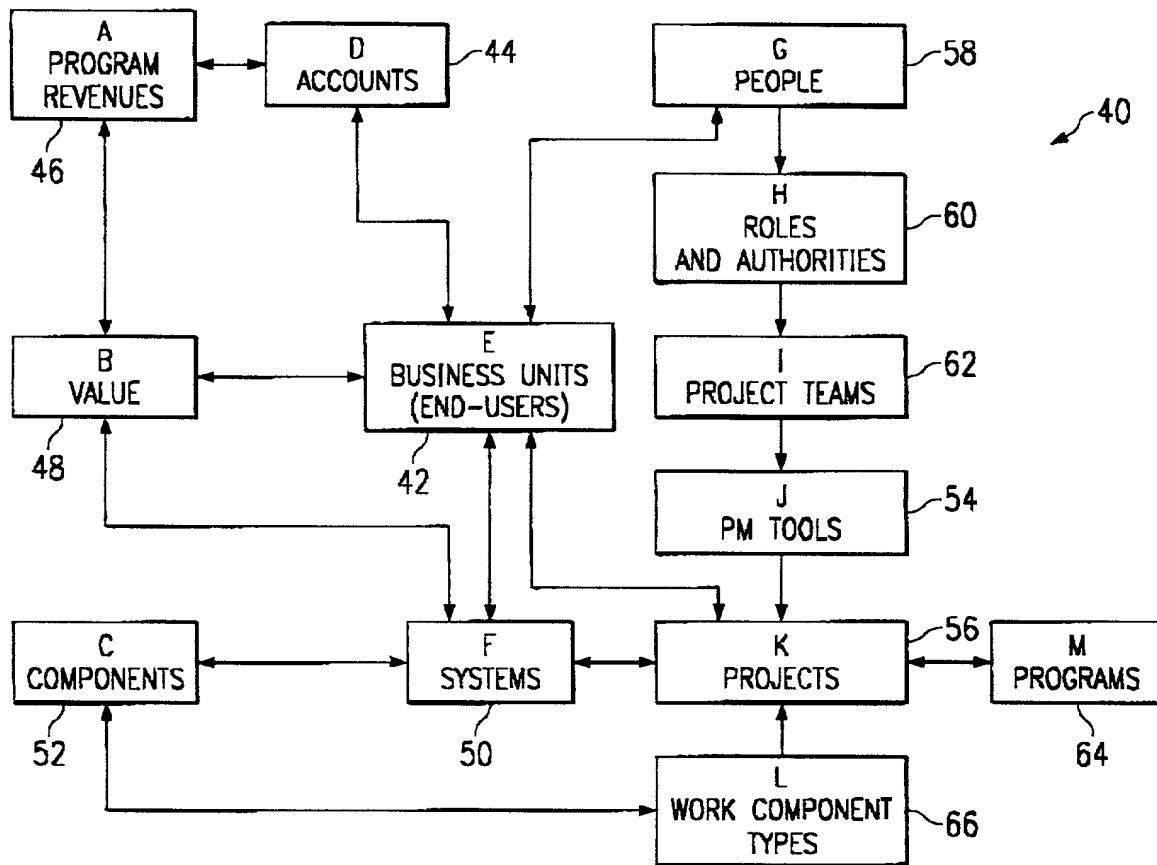


FIG. 4






Figure 5
09244550 020399

EDS

RMS Home

login

Person

[Add Person & Assign Roles](#)

[Update Authorizations](#)

[Update Personal Data](#)

[Change Password](#)

Account

[Add Account](#)

[Revise Account Data](#)

[Revise Account Forecasts](#)

[Update Account Actuals](#)

Project

[Add Project](#)

[Revise Basic Data and Forecasts](#)

[Update Budget and Labor Actuals](#)

[Update Schedules and Progress Actuals](#)

Reporting

[Extract Information](#)

09244550 020399

Figure 6

File Edit View Go Favorites Help

Back Stop Refresh Home Search Favorites History Charms Favorites Mail Edit

Address <https://webrip01.ses.cio.eds.com/year/2000/assignRoles.asp>

EDS

Add Person and Assign Roles

home

Review Current Roles

Person Assigned	Business Unit	Role Assigned
Ann Blue	Bob Smith	Technical Architect
Ann Blue	John Smith	Technical Architect
Ann Blue	John Smith	Project Manager
Sam Jones	Bob Smith	Project Manager
Sam Jones	Tom White	Technical Architect
Sam Jones	Joan Black	Technical Architect
Sam Jones	Joan Black	Program Coordinator for Unit
Tony Brown	Bob Smith	Program Coordinator for Unit

3 Add Person - Microsoft Internet Explorer

File Edit View Go Favorites Help

Back Forward Stop Refresh Home Search Favorites History Character Map Print

Address <https://webhip01.ses.cio.eds.com/year2000/addPerson.asp>

EDS

Add Person

home

First Name

Last Name

Address

ZIP/Postal Code

Mail Stop

Business Phone

Fax

Cellular Phone

Pager

E-Mail Address

Other Communication

User ID

Date

Local intranet core

Assign Person	Business Unit	Role to Assign
<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="text"/>	<input type="text"/>

ADD PERSON

DONE

Variable	Mean	SD	Min	Max
Age	38.5	10.2	22	55
Gender	Male	Female		
Marital status	Married	Single		
Education	High school	College		
Occupation	Manager	Worker		
Income	\$10,000	\$20,000		
Health status	Good	Fair		
Exercise frequency	Weekly	Monthly		
Stress level	Low	High		
Sleep quality	Good	Poor		
Dietary habits	Healthy	Unhealthy		
Alcohol consumption	None	Occasional		
Tobacco use	None	Regular		
Family size	2	3		
Work hours	40	50		
Commuting time	30	45		
Living space	Small	Large		
Neighborhood safety	Safe	Unsafe		
Access to green spaces	Yes	No		
Proximity to public transport	Close	Far		
Cost of housing	Low	High		
Quality of housing	Good	Poor		
Availability of services	High	Low		
Community involvement	Active	Passive		
Perceived social support	High	Low		
Life satisfaction	High	Low		
Overall well-being	Good	Poor		

EDS

Update Authorizations

home

Review Authorizations

Person Assigned	Update Authority	Surrogate
Joan Black	P	T
Ann Blue	P	T
Tony Brown	T	T
Sam Jones	T	T
Bob Smith	T	T
John Smith	T	T
Tom White	P	T

FileEditViewGoFavoritesHelp

BackForwardStopReloadHomeSearch

FavoritesHistoryChannelRegistrationMailPrintEdit

Address: https://webnrip01.ses.cio.eds.com/yea2000/AccountAdd.asp

EDS

Add Account

home

Account NameXYZ Company

Account ManagerSmith, John

CoordinatorJones, Henry

CountryArgentina

Account Start DateDate Format MM/DD/YYYY

Account End DateDate Format MM/DD/YYYY

Note: Check Boxes indicate Yes, for questions listed below.
Please only check boxes that relate to the Account being entered.

Contract and Customer Information

Does EDS now, or will you have any Y2K operational responsibility or obligation?

Have you verified Y2K operation responsibility with EDS Legal?

Enter EDS Legal contact

Financial Responsibility

Does the contract with your customer specifically state a responsibility for Y2K expenses?

Select responsibility for expenses: ☐ EDS ☐ Customer ☐ Both

Accounting Methodology

Is your contract accounted for under Percentage of Completion Accounting with Unbilled Revenue?

Done

Load Internet Data

Figure 11

09244550-020399

Forecasts

Overall Totals

Forecast by Month

Totals		Totals		Totals	
Months	Non Y2K Revenues	Non Y2K Expenses	Y2K Revenues	Y2K Non Proj. Expenses	
1/1998	0	0	0	0	
2/1998	0	0	0	0	
3/1998	0	0	0	0	
4/1998	0	0	0	0	
5/1998	0	0	0	0	
6/1998	0	0	0	0	
7/1998	0	0	0	0	
8/1998	0	0	0	0	
9/1998	0	0	0	0	
10/1998	0	0	0	0	
11/1998	0	0	0	0	
12/1998	0	0	0	0	
1/1999	0	0	0	0	

Figure 12

SECRET



Account Name XYZ Company

Actual Expenditures	Months	Non Y2K Revenues	Non Y2K Expenses	Y2K Revenues	Y2K Non Proj. Expenses
	1/1999	0	0	0	0
	12/1998	0	0	0	0
	12/1997	0	0	0	0
	12/1996	0	0	0	0
	12/1995	0	0	0	0
	12/1994	0	0	0	0
	12/1993	0	0	0	0
	12/1992	0	0	0	0
	12/1991	0	0	0	0
	12/1990	0	0	0	0
	12/1989	0	0	0	0
	12/1988	0	0	0	0
	12/1987	0	0	0	0
	Grand Total	0	0	0	0

Figure 13

EIS

Update Account Actuals

home

Account Name Account X
Account ID 1429

Months	NonY2kRev.\$	NonY2kExp.\$	Y2KRev.\$	Y2kNonProjExp\$	0\$
10/1998	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="checkbox"/>
11/1998	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="checkbox"/>
12/1998	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="checkbox"/>

Account Name Account Y
Account ID 1431

Months	NonY2kRev.\$	NonY2kExp.\$	Y2KRev.\$	Y2kNonProjExp\$	0\$
10/1998	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="checkbox"/>
11/1998	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="checkbox"/>
12/1998	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="checkbox"/>

Click the 0\$ check box if no data (zero) is to be reported for this month. This will remove the month from the worklist.

Figure 14

New Project - Microsoft Internet Explorer

FileEditViewGoFavoritesHelp

Back

Stop

Refresh

Home

Search

Favorites

History

Channels

Feeds

Mail

Print

Edit

Address: https://webnlp01.ses.cio.eds.com/year2000/NP103-BasicPrlrdo.asp

Link

EDS

Add Project

home

Project Name

Project Code

Account

Project Manager

Business Manager

Coordinator

Tech Architect/Owner

Must Start Date

Project Failure Date

Tactic

Impacting Program

Project A

123

Account X

John Adams

Julie White

Tom Smith

Steve Jones

09/18/1998

12/31/1999

Project in assessment tactic unknown

Funding Source

SAP Implementation

Technology Refresh

Funding %

Owner

Impact

Date

Load Internet zone

Figure 15A . 020399

Regular Unit Support	<input type="checkbox"/>	%	<input type="checkbox"/>	<input type="checkbox"/>
Year 2000 EDS Internal	<input type="checkbox"/>	%	<input type="checkbox"/>	<input type="checkbox"/>
Year 2000 Services for External Customers	<input type="checkbox"/>	%	<input type="checkbox"/>	<input type="checkbox"/>

Work Components

Component Description	Unit Count	Unit Description	Labor Effort %
Application Lines of Code		LOC	%
Business Partner Mgmt (e.g., Vendors)		Business Partners	%
Facilities Equipment		Embedded chip products	%
Mainframe HDW Devices		Devices	%
Mainframe Regions or Products		Products or Regions	%
Midrange HDW Devices		Devices	%
Midrange Regions or Products		Products or Regions	%
Network Routers, Hubs, Switches, etc.		Devices	%
Workstations		Workstations	%
Workstation SFW packages		Package installs	%

Contingency Costs

Year	Cost
2000	\$0
2001	\$0
2002	\$0

Figure 15B



Project Name

Project
Project ABC

Functional Area

Services provided to external customers

Country

Argentina

Argentina is not the default, it's just the first country in the list. Select the correct country.

Weights

Process	Impact
Lead	No impact
Plan	No impact
Manage	No impact
Market	No impact
Sell	No impact
Deliver	No impact

Project Notes

Next Cancel

Figure 15C

EDS

Project Milestone Data

home

Project Name

Project X

Tactic

Repair Existing System

Milestone Dates & Percent Completed

Milestones	Target Start	Actual Start	Target End	Actual End	% Completed
Assess					0
Modification					0
Test					0
Implement					0

Date Format MM/DD/YYYY

Next

Cancel

The number of milestones depends on the chosen tactic.

Figure 15D

66020-0541250



Project Name Project X

Overall Totals

Totals	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
--------	--------------------------------	--------------------------------	--------------------------------	--------------------------------	--------------------------------

Forecast by Month

Months	Hardware \$	Software \$	Labor \$	Other \$	FTEs
1/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
2/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
3/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
4/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
5/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
6/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
7/1999	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>
Current Totals	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>	<input type="text" value="0"/>

Figure 15E



Project Name Project X

Actual Expenditures		Months	Hardware \$	Software \$	Labor \$	Other \$	FTE (Mth)
		1/1999	0	0	0	0	0
		Current Totals	0	0	0	0	0

Figure 15F

EDS

Update Budget and Labor Actuals

home

Project Name Project A

Project ID	Months	Hardware \$	Software \$	Labor \$	Other \$	FTE (Months)	0\$
12							
Project Code	1/1999	0	0	0	0	0	<input type="checkbox"/>
12							

Project Name Project B

Project ID	Months	Hardware \$	Software \$	Labor \$	Other \$	FTE (Months)	0\$
15							
Project Code	1/1999	0	0	0	0	0	<input type="checkbox"/>
16							

Project Name Project C

Project ID	Months	Hardware \$	Software \$	Labor \$	Other \$	FTE (Months)	0\$
22							
Project Code	1/1999	0	0	0	0	0	<input type="checkbox"/>
23							

Project Name Project D

Project ID	Months	Hardware \$	Software \$	Labor \$	Other \$	FTE (Months)	0\$
26							
Project Code	1/1999	0	0	0	0	0	<input type="checkbox"/>
27							

Click the 0\$ check box if the costs were zero or no FTEs were used for the month. This will remove the items from your worklist.

Figure 16

Update Schedules and Progress Actuals

Home

Project Name Project A

Project ID
342
Project Code
518

Months	Milestone	Tar. Start	Tar. End	Act. Start	Act. End	% Compl.	N/C
1/1/99	Test	9/18/1998	1/1/1999	10/1/1998		70	✓
1/1/99	Implement	1/10/1999	2/15/1999			0	✓

Project Name Project B

Project ID
343
Project Code
519


Months	Milestone	Tar. Start	Tar. End	Act. Start	Act. End	% Compl.	N/C
1/1/99	Assess	9/1/1997	12/24/1997			0	✓
1/1/99	Modification	12/25/1997	4/17/1998			0	✓
1/1/99	Test	4/18/1998	9/1/1998			0	✓
1/1/99	Implement	11/8/1998	11/10/1998			0	✓

Project Name Project C

Project ID
348
Project Code
524

Months	Milestone	Tar. Start	Tar. End	Act. Start	Act. End	% Compl.	N/C
12/1/98	Assess	9/1/1997	12/24/1997	3/24/1997		98.7	✓
1/1/99	Assess	9/1/1997	12/24/1997	3/24/1997		98.7	✓
1/1/99	Gather	12/25/1997	4/17/1998	1/1/1998		0	✓

Local Internet Drive

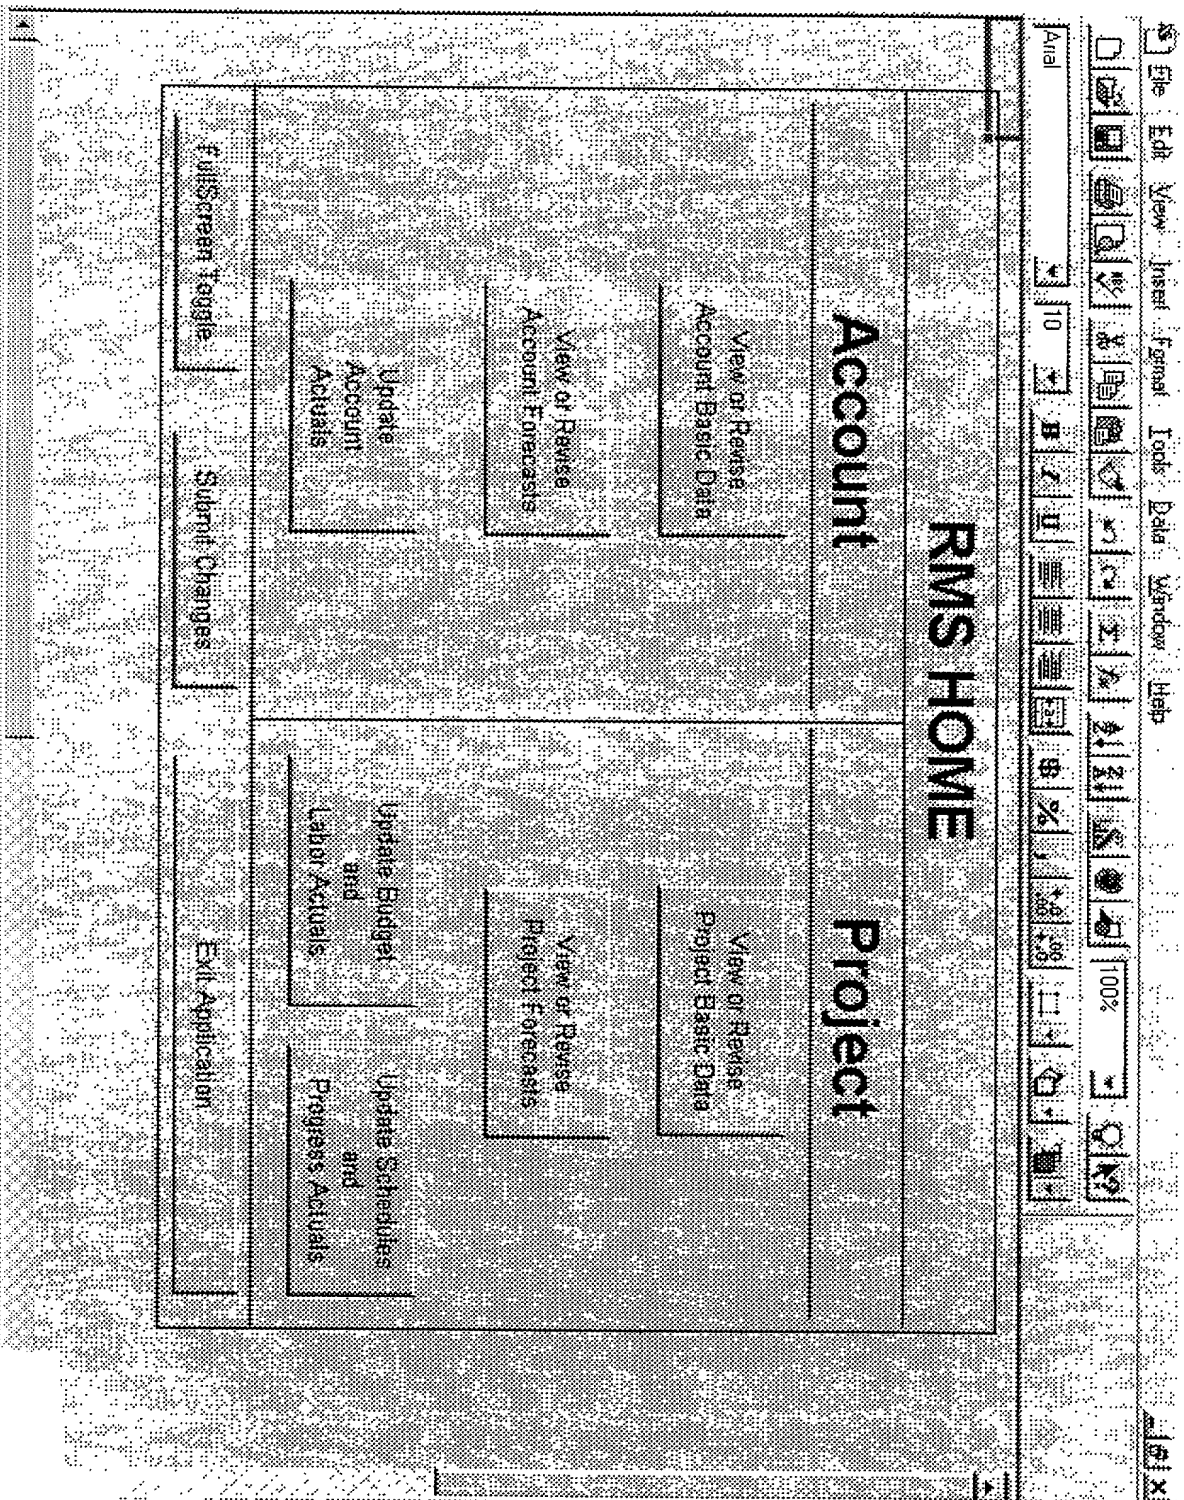

09244550 - 020399
Figure 18

FileEditViewInsertFormatToolsDataWindowHelp

Arial10BZU...100%

Cells that have not been updated

Data is in Error and must be changed before reporting

Informational: does not stop reporting

Data is valid and ready to report

Validate Data

Exit Module

Toggle Screen

View or Revise Account Forecasts

Account Name	Month	Non Y2K Revenue	Non Y2K Expenses	Y2K Non Project Expense	Y2K Revenues	Results
Account X	1/1/97					
Account X	2/1/97					
Account X	3/1/97					
Account X	4/1/97					
Account X	5/1/97					
Account X	6/1/97					
Account X	7/1/97					
Account X	8/1/97					
Account X	9/1/97					
Account X	10/1/97					
Account X	11/1/97					
Account X	12/1/97					

09244550.020399
Figure 19

Update Account Actuals

Cells that have not been updated

Data is in Error and must be changed before reporting

Informational - does not stop reporting

Data is valid and ready to report

Account Actuals View

☒ View Worksheet Only

☐ View Actuals

Validate Data

Exit Module

Toggle Screen

Account Name	Month	Non Y2K Revenue	Non Y2K Expenses	Y2K Non Project Expense	Y2K Revenues	Report 60,002 (Y/N)	Results
Account X	10/1/98	0	0	0	0	N	
Account X	11/1/98	0	0	0	0	N	
Account X	12/1/98	0	0	0	0	N	
Account X	10/1/98	0	0	0	0	N	
Account X	11/1/98	0	0	0	0	N	
Account X	12/1/98	0	0	0	0	N	
Account X	10/1/98	0	0	0	0	N	
Account X	11/1/98	0	0	0	0	N	
Account X	12/1/98	0	0	0	0	N	
Account X	10/1/98	0	0	0	0	N	
Account X	11/1/98	0	0	0	0	N	
Account X	12/1/98	0	0	0	0	N	

Tables									
Process		Function		Program		Role		Person	
ProcessID	ProcessDescr	FunctionID	FunctionDescr	ProgramID	ProgramDescr	RoleID	RoleDescr	PersonID	PersonDescr
Weight	WIDescr	FunctionAcctDescr	FunctionAcctID	ProgramAcctDescr	ProgramAcctID	RoleAcctDescr	RoleAcctID	PersonAcctDescr	PersonAcctID

Surrogate		Person		Country		MSCal		Tactic	
SurrogateID	SurrogateDescr	PersonID	PersonDescr	CountryID	CountryDescr	MSCalID	MSCalDescr	TacticID	TacticDescr
SurrogateAcctDescr	SurrogateAcctID	PersonAcctDescr	PersonAcctID	CountryAcctDescr	CountryAcctID	MSCalAcctDescr	MSCalAcctID	TacticAcctDescr	TacticAcctID

Burlnt		TypeMSCalXref		Tactic	
BurlntID	BurlntDescr	TypeMSCalXrefID	TypeMSCalXrefDescr	TacticID	TacticDescr
BurlntAcctDescr	BurlntAcctID	TypeMSCalXrefAcctDescr	TypeMSCalXrefAcctID	TacticAcctDescr	TacticAcctID

Assignment		BUProcWght		TacticMS	
AssignmentID	AssignmentDescr	BUProcWghtID	BUProcWghtDescr	TacticMSID	TacticMSDescr
AssignmentAcctDescr	AssignmentAcctID	BUProcWghtAcctDescr	BUProcWghtAcctID	TacticMSAcctDescr	TacticMSAcctID

Account		AccountForecast	
AccountID	AccountDescr	AccountForecastID	AccountForecastDescr
AccountAcctDescr	AccountAcctID	AccountForecastAcctDescr	AccountForecastAcctID

Component		System		Project	
ComponentID	ComponentDescr	SystemID	SystemDescr	ProjectID	ProjectDescr
ComponentAcctDescr	ComponentAcctID	SystemAcctDescr	SystemAcctID	ProjectAcctDescr	ProjectAcctID


ProfForecast		WorkComp		ProjectForecast	
ProfForecastID	ProfForecastDescr	WorkCompID	WorkCompDescr	ProjectForecastID	ProjectForecastDescr
ProfForecastAcctDescr	ProfForecastAcctID	WorkCompAcctDescr	WorkCompAcctID	ProjectForecastAcctDescr	ProjectForecastAcctID

TransLog		ContingencyCost		ProjectForecastHistory	
TransLogID	TransLogDescr	ContingencyCostID	ContingencyCostDescr	ProjectForecastHistoryID	ProjectForecastHistoryDescr
TransLogAcctDescr	TransLogAcctID	ContingencyCostAcctDescr	ContingencyCostAcctID	ProjectForecastHistoryAcctDescr	ProjectForecastHistoryAcctID

CSR		CSRShortDescr		CSRStartDate	
CSRID	CSRDescr	CSRShortDescrID	CSRShortDescrDescr	CSRStartDateID	CSRStartDateDescr
CSRAcctDescr	CSRAcctID	CSRShortDescrAcctDescr	CSRShortDescrAcctID	CSRStartDateAcctDescr	CSRStartDateAcctID

Figure 21

FIG. 22B

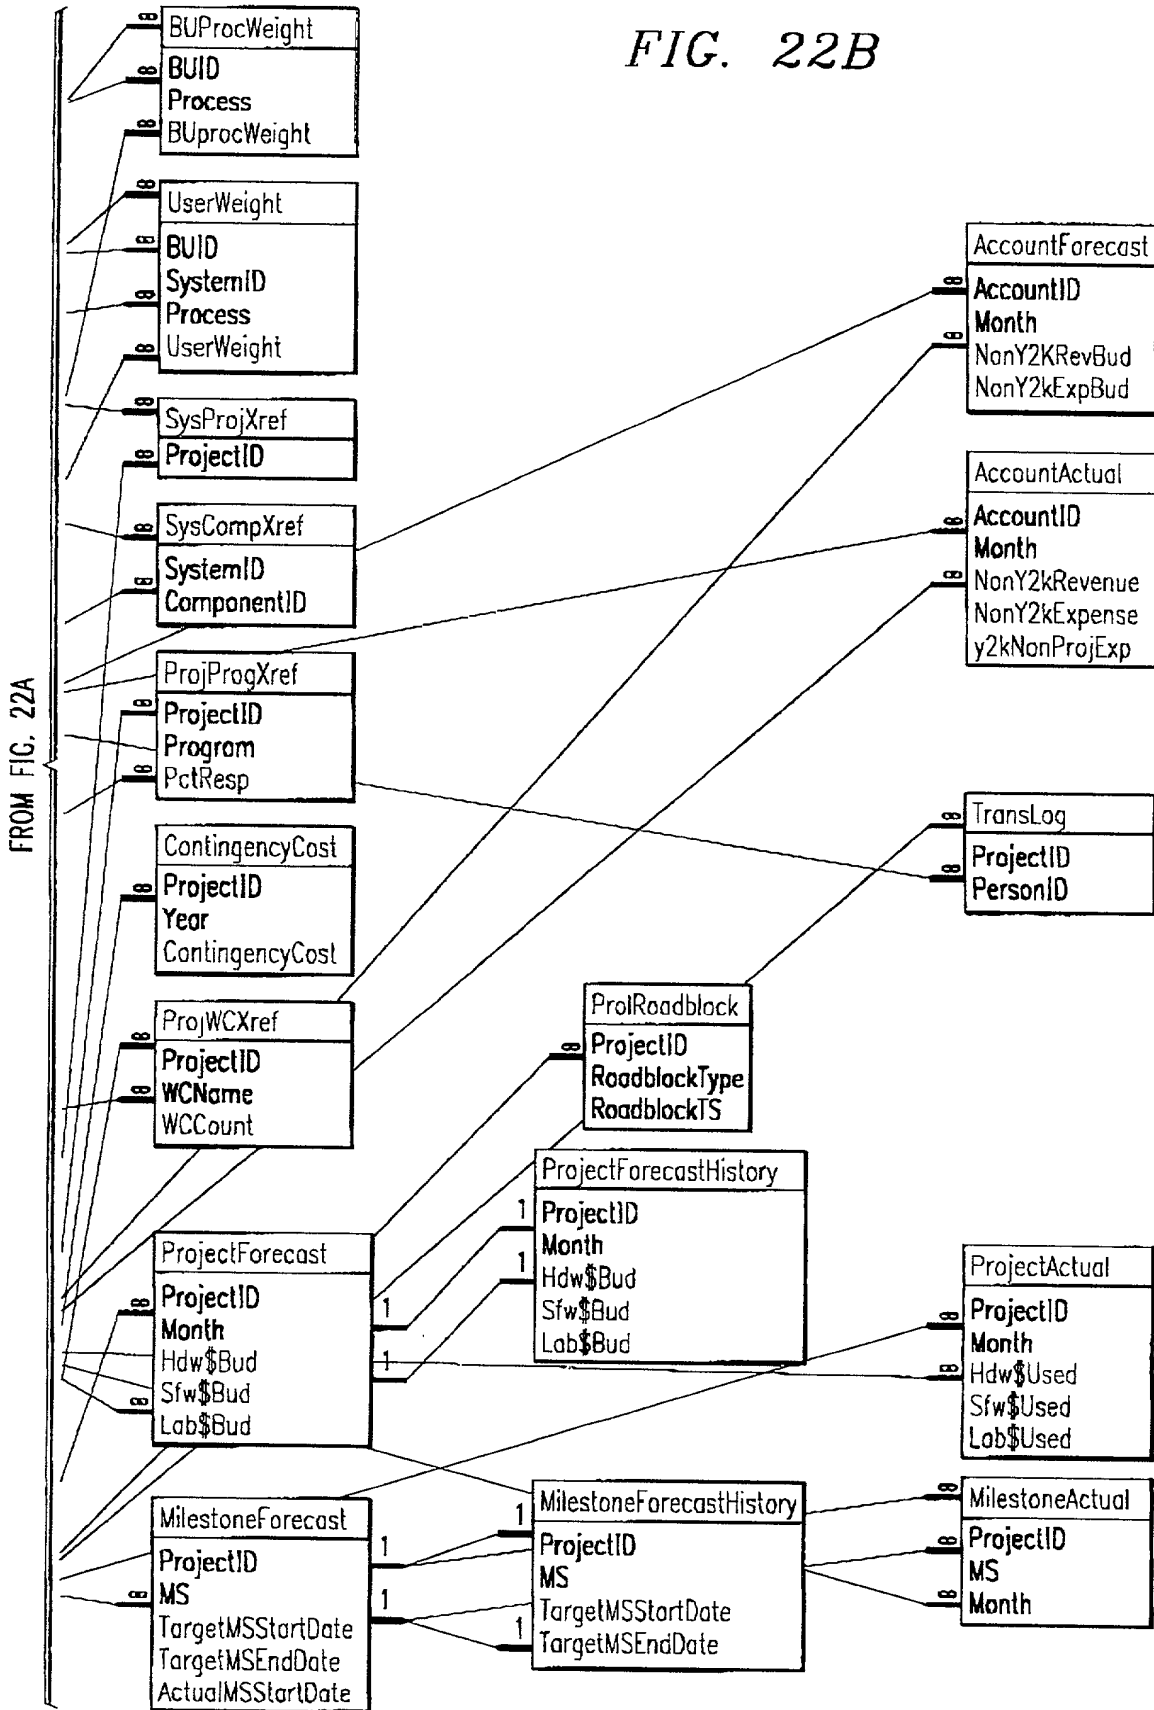

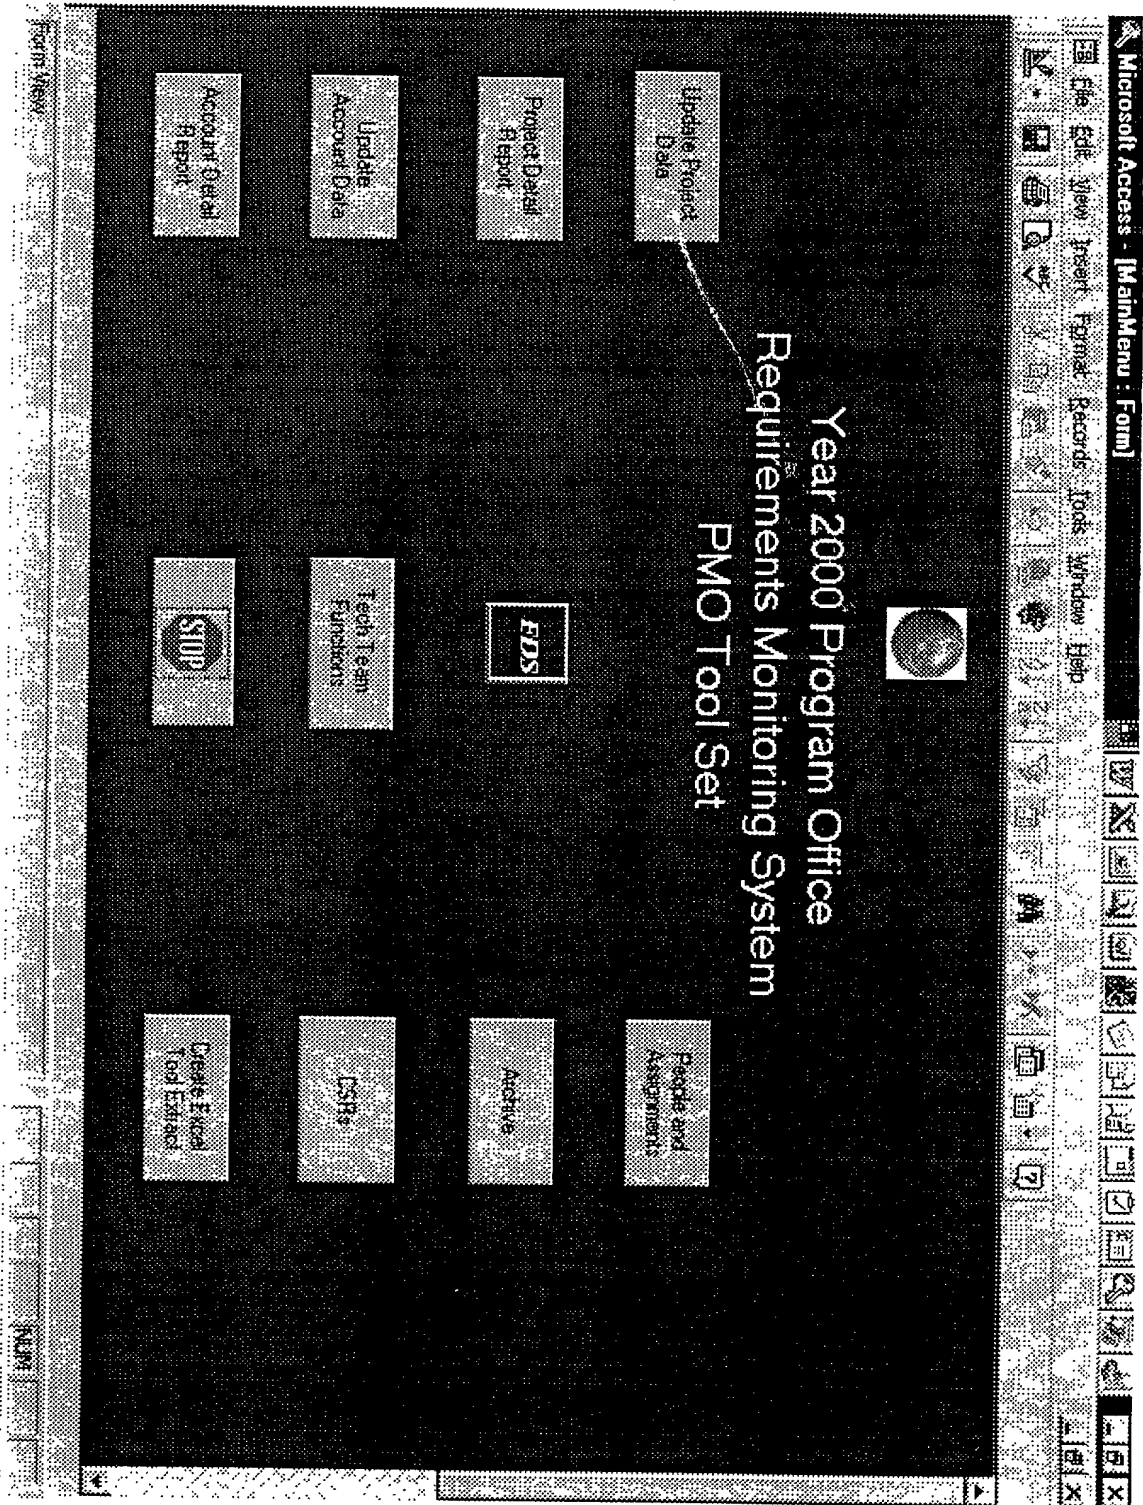


Figure 23

Microsoft Access - [ProjectSelectionCriteria : Form]

File Edit View Project Format Records Tools Window Help

Project Selection Criteria

Internal/External

Active/Pending

BUILD

Coordinator

Project Manager

Show Projects

Return to Main Menu

Record: 1 of 1

Form View

Figure 24

09244550 . 020399

Figure 25[illegible]

Project Forecasts						
Project ID		1		Return to Project		
Month	Hardware	Software	Labor	Other	FTEs	
9/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
9/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
7/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
5/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
5/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
4/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
3/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
2/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	
1/1/98	\$0.00	\$0.00	\$76.92	\$0.00	0	

Figure 26

Microsoft Access - [Milestone Dates]

File Edit View Insert Format Records Tools Window Help

ProjectID:

Filter:

Milestone Description	Target Start	Actual Start	Target End	Actual End
Assess	9/1/97		12/24/97	
Test	1/25/97		1/25/97	
Implement	4/1/98		9/1/98	

Form View

Figure 27

09244550.020399

Microsoft Access - [Milestone Actuals]

File Edit View Insert Format Records Tools Window Help

Properties: [ID] [Return to Field]

Fields: Test Only

Milestone Description	Month	Percent Complete
Assess	10/1/98	0.00%
Assess	11/1/98	0.00%
Test	10/1/98	0.00%
Test	11/1/98	0.00%
Implement	10/1/98	0.00%
Implement	11/1/98	0.00%

Form View

Figure 28

Microsoft Access - [ProjProgXref]

File Edit View Project Format Records Tools Window Help

ProjectID Program PatResp PrimanProg

1	Y2K	100.00%	Y
*			

Record 1 of 1 (Filtered)

Form View

Print

Menu

Figure 29

09244550-020399

Microsoft Access - [DetailReportData : Form]

File Edit View Insert Format Records Tools Window Help

Create Project Detail Report

- 1 Select type of projects: internal, external, or combined. One option must be highlighted in black.
- 2 Select a value for one of the fields below and click on the button to the right of the selection.

Select	<input type="text"/>	Select Report	<input type="text"/>
BUILD	<input type="text"/>	BUILD Report	<input type="text"/>
Coordinator	<input type="text"/>	Coordinator Report	<input type="text"/>
Project Number	<input type="text"/>	Project Report	<input type="text"/>

- 3 To output report to Excel Spreadsheet, click button at right after running report and verifying its contents.

Record: 1 of 1

Form View

Figure 30

09244550.020399

DECLARATION AND POWER OF ATTORNEY

As a below named inventor, I declare that:

My residence, post office address and citizenship are as stated below next to my name; that I believe I am the original, first and sole inventor (if only one name is listed below) or an original, first and joint inventor (if plural names are listed below) of the subject matter which is claimed and for which a patent is sought on the invention or design entitled *System and Method of Managing a Program Office*, the specification of which is attached hereto; that I have reviewed and understand the contents of the above-identified specification, including the claims, as amended by any amendment referred to above; and that I acknowledge the duty to disclose to the U.S. Patent and Trademark Office all information known to me to be material to patentability as defined in 37 C.F.R. § 1.56.

I hereby claim foreign priority benefits under 35 U.S.C. § 119 of any foreign application(s) for patent or inventor's certificate listed below and have also identified below any foreign application(s) for patent or inventor's certificate having a filing date before that of the application on which priority is claimed:

<u>Number</u>	<u>Country</u>	<u>Date Filed</u>	<u>Priority Claimed (Yes) (No)</u>
-----NONE-----			

I hereby claim the benefit under 35 U.S.C. § 120 of any United States application(s) listed below and, insofar as the subject matter of each of the claims of this application is not disclosed in the prior United States application(s) in the manner provided by the first paragraph of 35 U.S.C. § 112, I acknowledge the duty to disclose to the U.S. Patent and Trademark Office all information known to me to be material to patentability as defined in 37 C.F.R. § 1.56 which became available between the filing date of the prior application(s) and the national or PCT international filing date of this application:

<u>Application Serial Number</u>	<u>Date Filed</u>	<u>Status</u>
-----NONE-----		

I hereby appoint:

L. Joy Griebenow

Reg. No. 33,704

of Electronic Data Systems Corporation, and the following

Jerry W. Mills	Reg. No. 23,005
Robert M. Chiaviello, Jr.	Reg. No. 32,461
Ann C. Livingston	Reg. No. 32,479
Thomas R. Felger	Reg. No. 28,842
Charles S. Fish	Reg. No. 35,870
Wei Wei Jeang	Reg. No. 33,305
Kevin J. Meek	Reg. No. 33,738
T. Murray Smith	Reg. No. 30,222
Barton E. Showalter	Reg. No. 38,302
David G. Wille	Reg. No. 38,363
Bradley P. Williams	Reg. No. 40,227
Terry J. Stalford	Reg. No. 39,522
Christopher W. Kennerly	Reg. No. 40,675
Harold E. Meier	Reg. No. 22,428
Alexander B. Ching	Reg. No. 41,669
Douglas M. Kubehl	Reg. No. 41,915
Samir A. Bhavsar	Reg. No. 41,617
Thomas R. Nesbitt, Jr.	Reg. No. 22,075
James J. Maune	Reg. No. 26,946
Roger J. Fulghum	Reg. No. 39,678
Rodger L. Tate	Reg. No. 27,399
Scott F. Partridge	Reg. No. 28,142
James B. Arpin	Reg. No. 33,470
James Remenick	Reg. No. 36,902
Jay B. Johnson	Reg. No. 38,193
Robert W. Holland	Reg. No. 40,020
Floyd B. Chapman	Reg. No. 40,555
Randall W. Mishler	Reg. No. 42,006
Robert A. King	Reg. No. 42,738
James L. Baudino	Reg. No. P43,486
Scott T. Morris	Reg. No. P43,818
Tara D. Knapp	Reg. No. P43,723

all of the firm of Baker & Botts, L.L.P., my attorneys with full power of substitution and revocation, to prosecute this application and to transact all business in the United States Patent and Trademark Office connected therewith, and to file and prosecute any international patent applications filed thereon before any international authorities.

Send Correspondence To:

L. Joy Griebenow, Esq.
Electronic Data Systems
Corporation
5400 Legacy Drive, H3-3A-05
Plano, Texas 75024

Direct Telephone Calls To:

L. Joy Griebenow, Esq.
at (972) 605-5567
Attorney Docket No. 64-99-001

I declare that all statements made herein of my own knowledge are true and that all statements made on information and belief are believed to be true; and further that these statements were made with the knowledge that willful false statements and the like so made are punishable by fine or imprisonment, or both, under Section 1001 of Title 18 of the United States Code, and that such willful false statements may jeopardize the validity of the application or any patent issuing thereon.

Full name of the first inventor

Harriet E. Brichta

Inventor's signature

Harriet E. Brichta

Date

2/3/99

Residence (City, County, State)

Plano, Collin, Texas

Citizenship

United States of America

Post Office Address

6553 Osage Trail
Plano, Texas 75023

Full name of the second inventor

Floyd Phillip Littlefield, Jr.

Inventor's signature

Floyd Phillip Littlefield, Jr.

Date

2/3/99

Residence (City, County, State)

Wylie, Collin, Texas

Citizenship

United States of America

Post Office Address

1203 Butler Road
Wylie, Texas 75098

Full name of the third inventor

Bruce W. Bradbury

Inventor's signature

Date

Residence (City, County, State)

Allen, Collin, Texas

Citizenship

United States of America

Post Office Address

813 Willow Brook Drive
Allen, Texas 75002

Full name of the fourth inventor

Iveoma C. Eriken

Inventor's signature

Iveoma Eriken

Date

2/3/99

Residence (City, County, State)

Carrollton, Dallas, Texas

Citizenship

United States of America

Post Office Address

2107 Columbian Club Drive
Carrollton, Texas 75006

Full name of the fifth inventor

Julio A. Rodriguez

Inventor's signature

Date

Residence (City, County, State)

Garland, Dallas, Texas

Citizenship

United States of America

Post Office Address

1810 Quail Hill Circle
Garland, Texas 75040

094455-02099
66E020 0554260
